

ID	Task Name	Duration	Start	Finish	Predecessors
1	BAU releases	136 days	03/02/14 08:00	11/08/14 05:00	
2	NG3 -WA edition (14.03)	33 days	03/02/14 08:00	19/03/14 05:00	
8	NG3 - WA extensions	73 days	07/03/14 08:00	17/06/14 05:00	
17	Rural migration (importer) MAY	76 days	01/04/14 08:00	15/07/14 05:00	
28					
29	BAU - NEWS and Radio National Consolidation	77 days	10/04/14 08:00	25/07/14 05:00	
59					
82					
83	POST deployment	11 days	28/07/14 08:00	11/08/14 05:00	
87					
88	Is chef available ?	0 days	01/08/14 08:00	01/08/14 08:00	a
89	deployment plan for Phase 2	0 days	01/07/14 08:00	01/07/14 08:00	a
90					
91					
92	Phase 2 milestones	136 days	23/05/14 08:00	28/11/14 05:00	
93	Merged code base	46 days	23/05/14 08:00	25/07/14 05:00	
94	Merged code base ready for test	0 days	23/05/14 08:00	23/05/14 08:00	a47SS+1 day
95	Merged code in Prod	0 days	25/07/14 05:00	25/07/14 05:00	p81SS
96	P2 - R11	66 days	27/06/14 08:00	26/09/14 05:00	
97	R11 test complete	0 days	27/06/14 08:00	27/06/14 08:00	a

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary	External Tasks	
	Split		Manual Task	External Milestone	
	Milestone		Duration-only	Deadline	
	Summary		Manual Summary Rollup	Progress	
	Project Summary		Manual Summary	Manual Progress	
	Inactive Task		Start-only		
	Inactive Milestone		Finish-only		

ID	Task Name	Duration	Start	Finish	Predecessors
98	R11 code in Prod	0 days	26/09/14 05:00	26/09/14 05:00	p131
99	P2 - R12	40 days	01/08/14 05:00	26/09/14 05:00	
100	R12 test complete	0 days	01/08/14 05:00	01/08/14 05:00	
101	R12 code in Prod	0 days	26/09/14 05:00	26/09/14 05:00	p131
102	P2 - R13	40 days	05/09/14 05:00	31/10/14 05:00	
103	R13 test complete	0 days	05/09/14 05:00	05/09/14 05:00	
104	R13 code in Prod	0 days	31/10/14 05:00	31/10/14 05:00	p142
105	P2 - R14	20 days	03/10/14 05:00	31/10/14 05:00	
106	R14 test complete	0 days	03/10/14 05:00	03/10/14 05:00	
107	R14 code in Prod	0 days	31/10/14 05:00	31/10/14 05:00	p142
108	P2 - R15	21 days	31/10/14 08:00	28/11/14 05:00	
109	R15 test complete	0 days	31/10/14 08:00	31/10/14 08:00	a
110	R15 code in Prod	0 days	28/11/14 05:00	28/11/14 05:00	p153
111	Stage 1 available in Production	0 days	28/11/14 05:00	28/11/14 05:00	p108
112					
113	Prod Releases	139 days	03/06/14 08:00	12/12/14 05:00	
114	BAU Release - AUG (14.08 - Rural + Chef only + Parts of R11 & 12)	30 days	21/07/14 08:00	29/08/14 05:00	
115	Merge code	5 days	21/07/14 08:00	25/07/14 05:00	
116	Regression test	15 days	28/07/14 08:00	15/08/14 05:00	p115
117	Performance test	10 days	04/08/14 08:00	15/08/14 05:00	p116SS+5 days

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors
118	UAT	5 days	18/08/14 08:00	22/08/14 05:00	117
119	Deploy to Prod	5 days	25/08/14 08:00	29/08/14 05:00	118
120	Release 14.08 in Prod	0 days	29/08/14 05:00	29/08/14 05:00	119
121	BAU Release - SEPT (14.09 - Parts of R12 & 13)	84 days	03/06/14 08:00	26/09/14 05:00	
122	BAU dev	10 days	03/06/14 08:00	16/06/14 05:00	
123	BAU Test	10 days	17/06/14 08:00	30/06/14 05:00	122
124	BAU perf test	5 days	01/07/14 08:00	07/07/14 05:00	123
125	BAU UAT	1 day	08/07/14 08:00	08/07/14 05:00	124
126	Merge code	5 days	25/08/14 08:00	29/08/14 05:00	118, 124
127	Regression test	10 days	01/09/14 08:00	12/09/14 05:00	126
128	Performance test	5 days	08/09/14 08:00	12/09/14 05:00	127SS+5 days
129	UAT	5 days	15/09/14 08:00	19/09/14 05:00	128
130	Deploy to Prod	5 days	22/09/14 08:00	26/09/14 05:00	129
131	Release 14.09 in Prod	0 days	26/09/14 05:00	26/09/14 05:00	130
132	BAU Release - OCT (14.10 - 14 + Rest of R13)	83 days	09/07/14 08:00	31/10/14 05:00	
133	BAU dev	10 days	09/07/14 08:00	22/07/14 05:00	125
134	BAU Test	10 days	23/07/14 08:00	05/08/14 05:00	133
135	BAU perf test	5 days	06/08/14 08:00	12/08/14 05:00	134
136	BAU UAT	1 day	13/08/14 08:00	13/08/14 05:00	135
137	Merge code	5 days	29/09/14 08:00	03/10/14 05:00	130, 136

Project: WCMS BAU RELEASES V3
Date: 01/03/18 03:17 pm

Task 

Split 

Milestone 

Summary 

Project Summary 

Inactive Task 

Inactive Milestone 

Inactive Summary 

Manual Task 

Duration-only 

Manual Summary Rollup 

Manual Summary 

Start-only 

Finish-only 

External Tasks 

External Milestone 

Deadline 

Progress 

Manual Progress 

ID	Task Name	Duration	Start	Finish	Predecessors
138	Regresssion test	10 days	06/10/14 08:00	17/10/14 05:00	p137
139	Performance test	5 days	13/10/14 08:00	17/10/14 05:00	p138SS+5 days
140	UAT	5 days	20/10/14 08:00	24/10/14 05:00	p139
141	Deploy to Prod	5 days	27/10/14 08:00	31/10/14 05:00	p140
142	Release 14.10 in Prod	0 days	31/10/14 05:00	31/10/14 05:00	p141
143	BAU Release - NOV (14.11 - R15)	77 days	14/08/14 08:00	28/11/14 05:00	
144	BAU dev	10 days	14/08/14 08:00	27/08/14 05:00	p136
145	BAU Test	10 days	28/08/14 08:00	10/09/14 05:00	p144
146	BAU perf test	5 days	11/09/14 08:00	17/09/14 05:00	p145
147	BAU UAT	1 day	18/09/14 08:00	18/09/14 05:00	p146
148	Merge code	5 days	27/10/14 08:00	31/10/14 05:00	p140, 147
149	Regresssion test	10 days	03/11/14 08:00	14/11/14 05:00	p148
150	Performance test	5 days	10/11/14 08:00	14/11/14 05:00	p149SS+5 days
151	UAT	5 days	17/11/14 08:00	21/11/14 05:00	p150
152	Deploy to Prod	5 days	24/11/14 08:00	28/11/14 05:00	p151
153	Release 14.11 in Prod	0 days	28/11/14 05:00	28/11/14 05:00	p152
154	BAU Release - DEC (14.12)	15 days	24/11/14 08:00	12/12/14 05:00	
155	Bug fixes	5 days	24/11/14 08:00	28/11/14 05:00	p151
156	Regresssion test	5 days	24/11/14 08:00	28/11/14 05:00	p151
157	Performance test	5 days	24/11/14 08:00	28/11/14 05:00	p151

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID	Task Name	Duration	Start	Finish	Predecessors
158	UAT	5 days	01/12/14 08:00	05/12/14 05:00	157, 156
159	Deploy to Prod	5 days	08/12/14 08:00	12/12/14 05:00	158
160	Release 14.12 in Prod	0 days	12/12/14 05:00	12/12/14 05:00	159

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

[illegible]


Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			


[illegible]

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

Resource Names	% Complete	Jan '14		10 Feb '14				24 Feb '14				10 Mar '14				24 Mar '14				07 Apr '14				21 Apr '14				05 May '14				19 May '14				02 Jun '14				16 Jun '14			
		S	F	W	M	S	T	T	S	F	W	M	S	T	T	S	F	W	M	S	T	T	S	F	W	M	S	T	T	S	F	W	M	S	T	T							
	0%																																										
	0%																																										
	0%																																										
Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task					Inactive Summary								External Tasks																													
	Split					Manual Task								External Milestone																													
	Milestone					Duration-only								Deadline																													
	Summary					Manual Summary Rollup								Progress																													
	Project Summary					Manual Summary								Manual Progress																													
	Inactive Task					Start-only																																					
	Inactive Milestone					Finish-only																																					
Page 10																																											

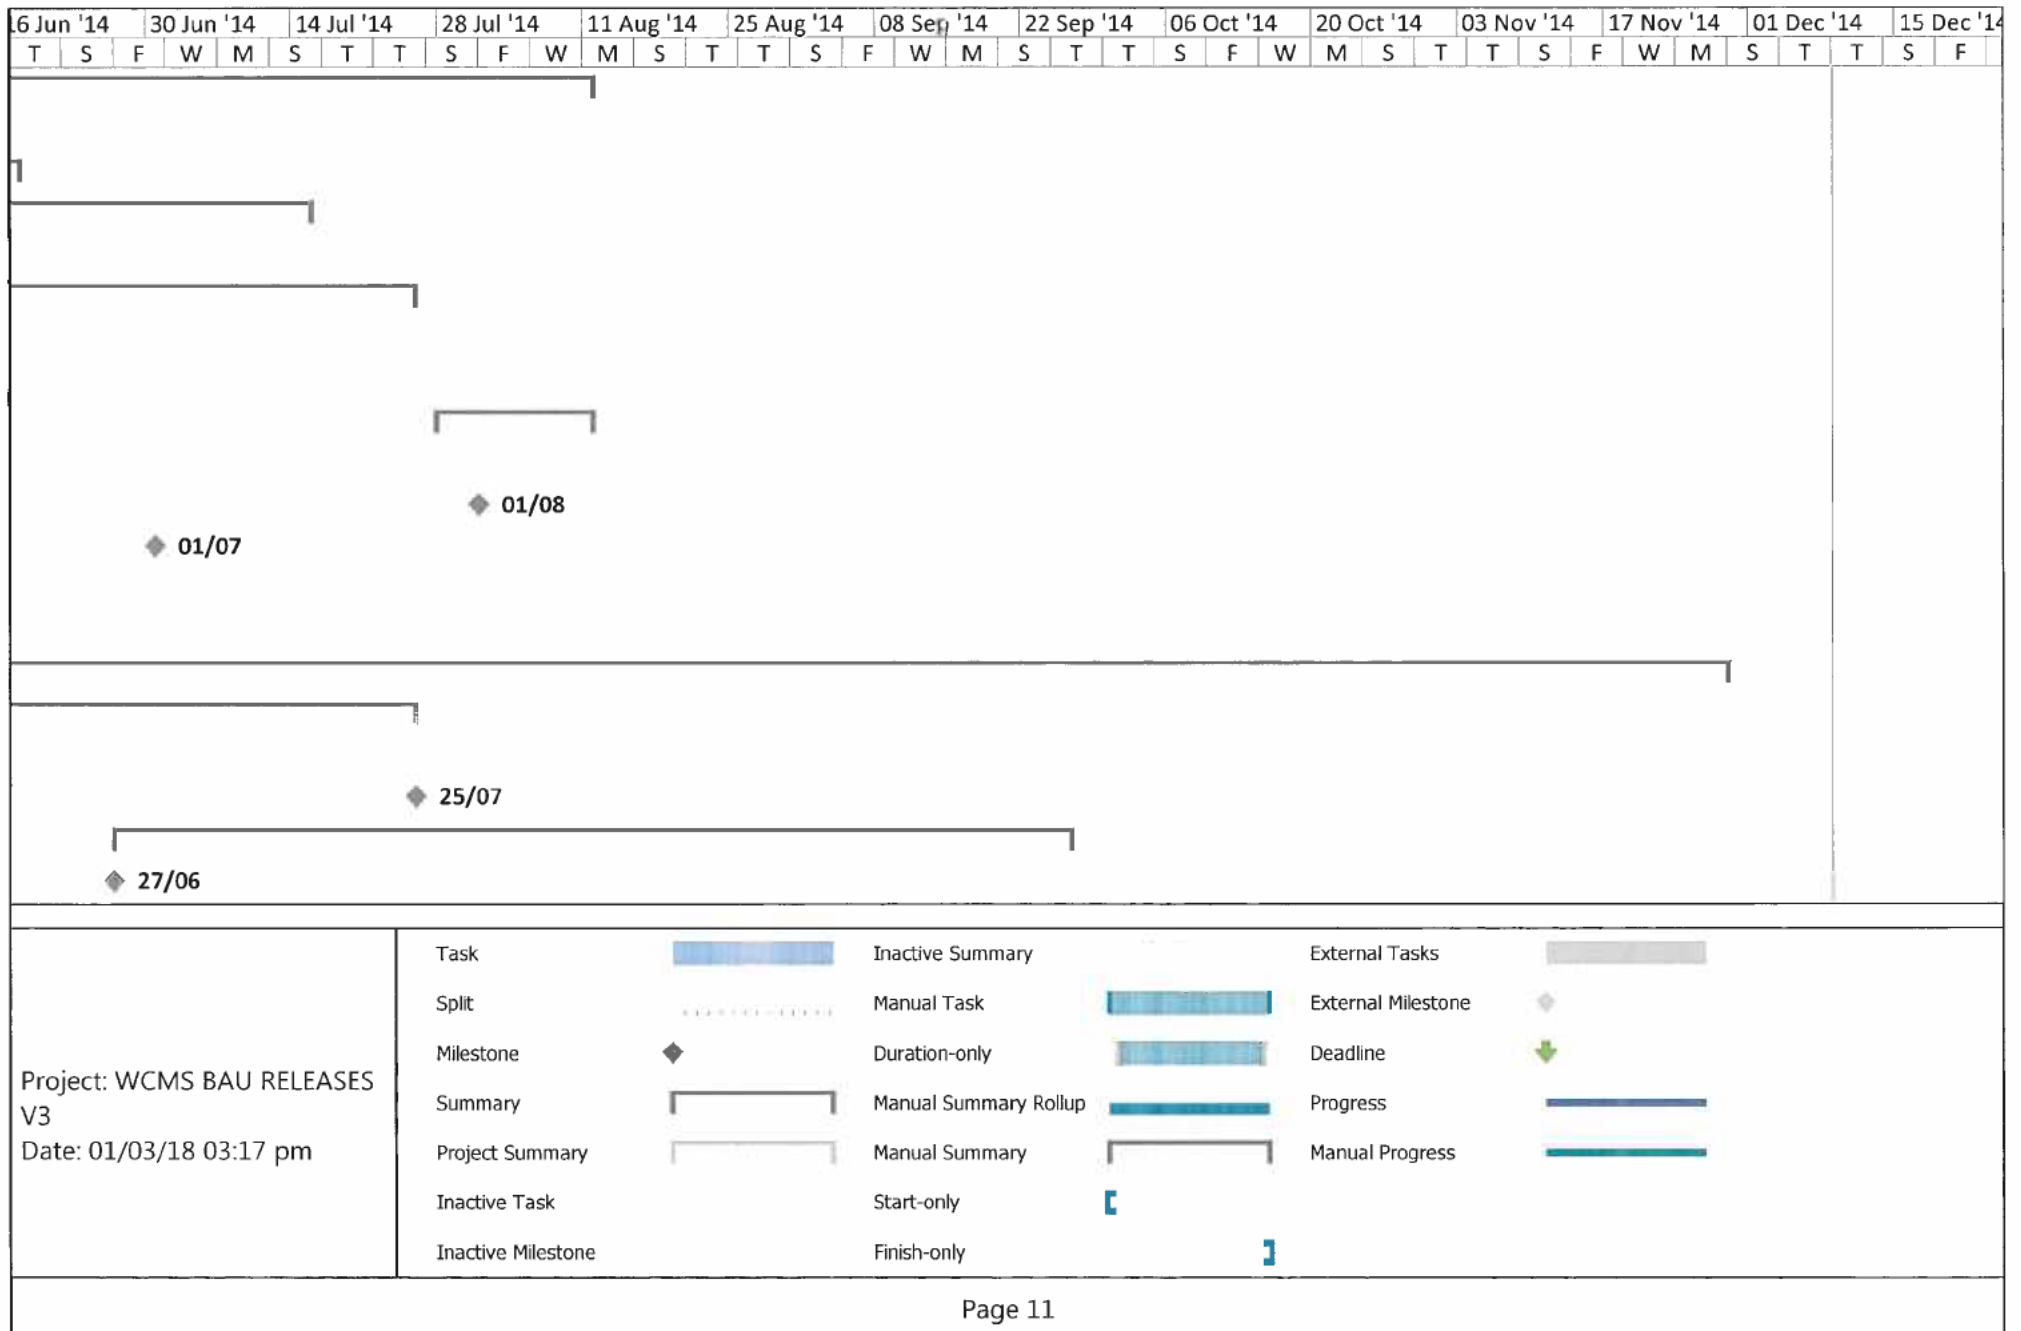




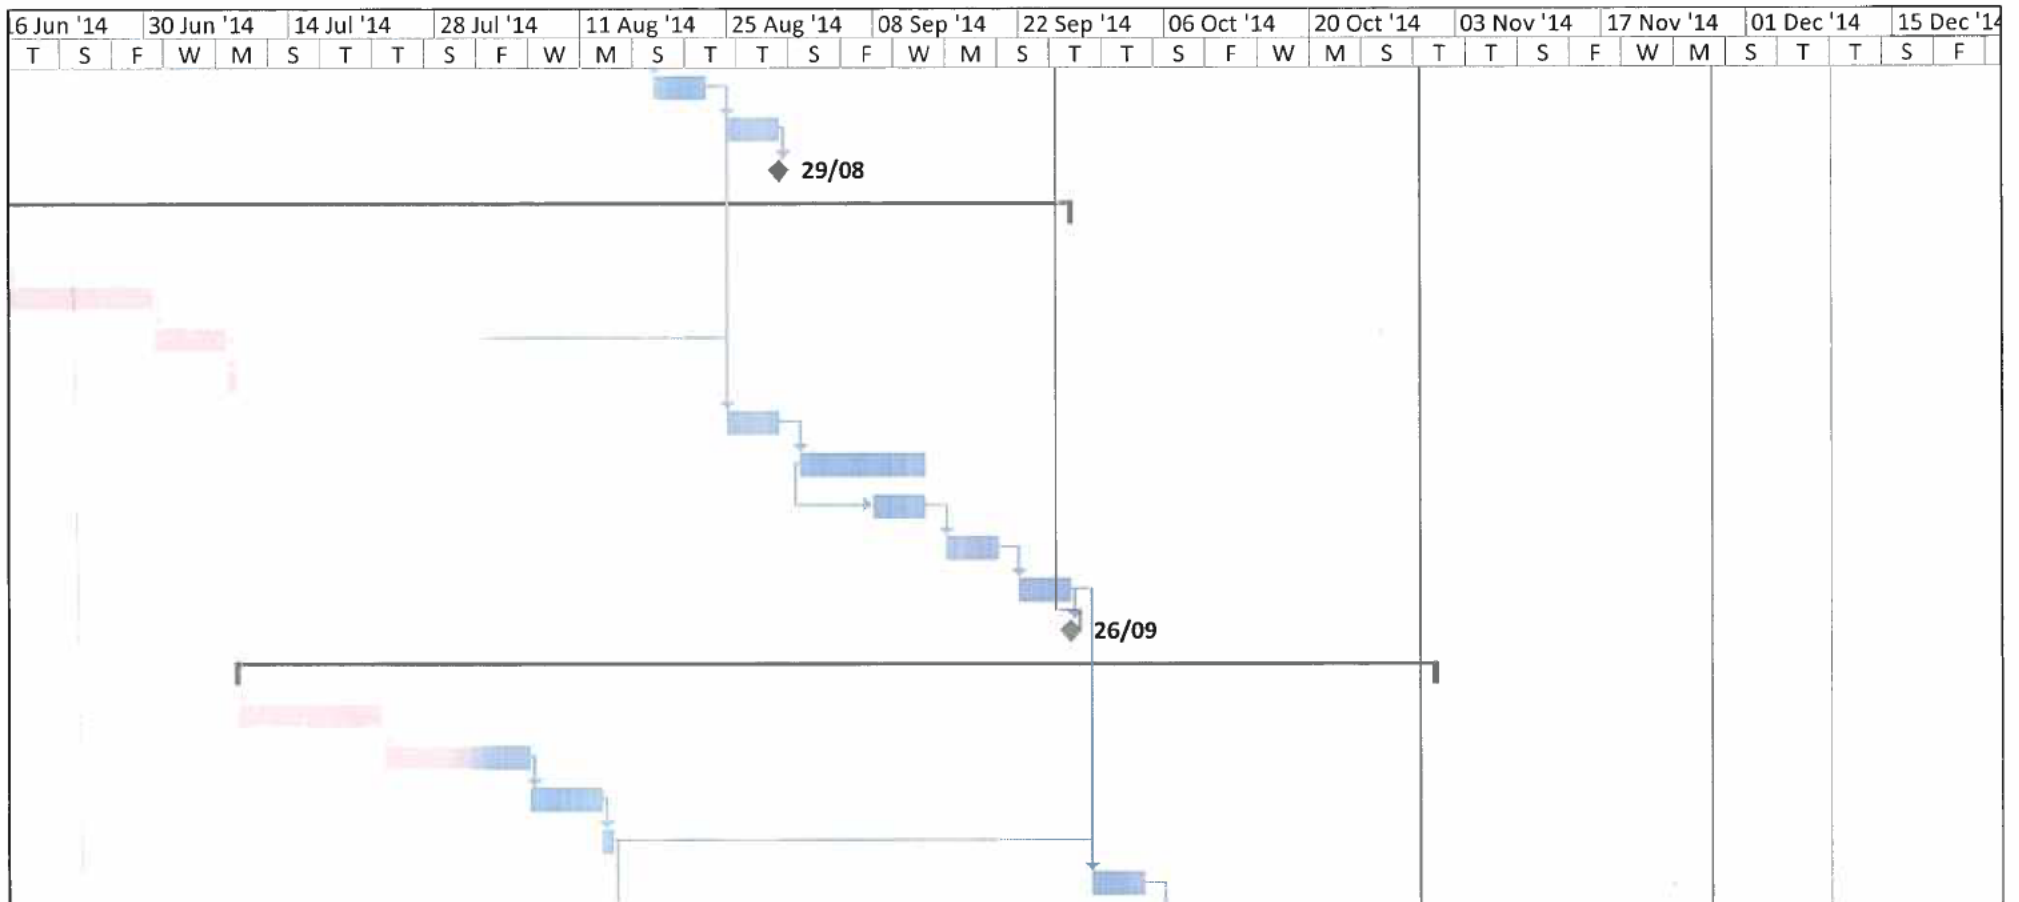

Project: WCMS BAU RELEASES
V3

Date: 01/03/18 03:17 pm

Task		Inactive Summary		External Tasks	
Split		Manual Task		External Milestone	
Milestone		Duration-only		Deadline	
Summary		Manual Summary Rollup		Progress	
Project Summary		Manual Summary		Manual Progress	
Inactive Task		Start-only			
Inactive Milestone		Finish-only			

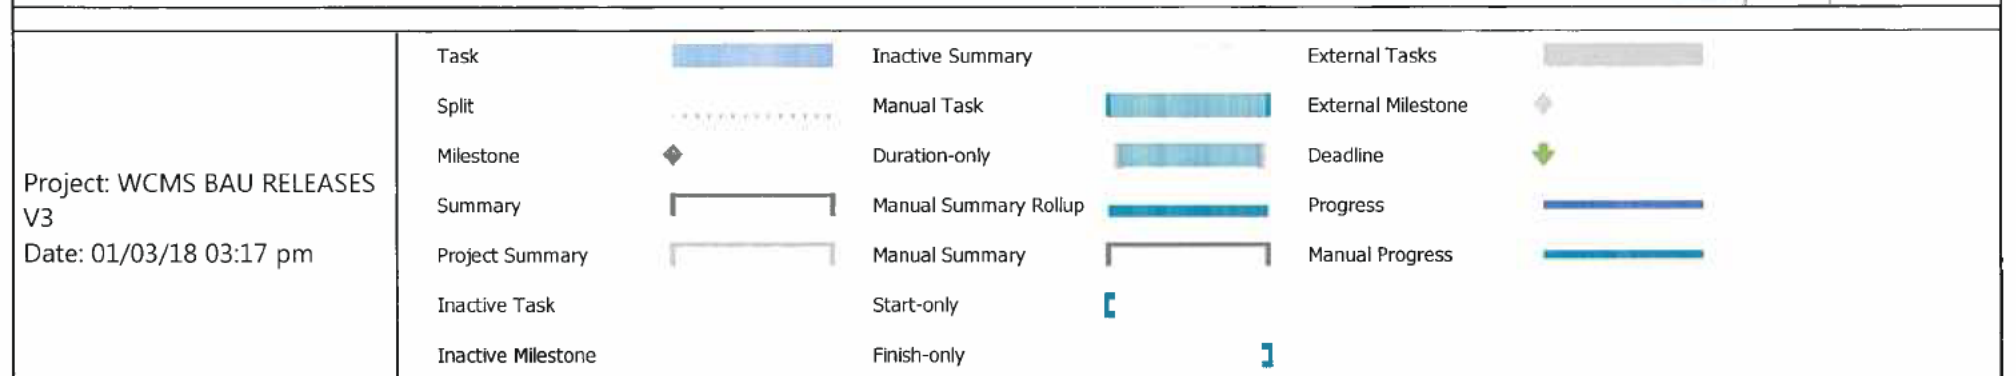

Project: WCMS BAU RELEASES V3 Date: 01/03/18 03:17 pm	Task		Inactive Summary		External Tasks	
	Split		Manual Task		External Milestone	
	Milestone		Duration-only		Deadline	
	Summary		Manual Summary Rollup		Progress	
	Project Summary		Manual Summary		Manual Progress	
	Inactive Task		Start-only			
	Inactive Milestone		Finish-only			

ID		Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	03 Feb '14									10
									S	M	T	W	T	F	S	S	M	
1			BAU releases	246 days	03/02/14 08:	12/01/15 05:												
2	✓		NG3 -WA edition	33 days	03/02/14 08:	19/03/14 05:												
3	✓		NG3 Dev	10 days	03/02/14 08:	14/02/14 05:		Andrew R, Shilpi,										
4	✓		NG3 testing	10 days	17/02/14 08:	28/02/14 05:	3	Kris R, Test 1 Envi										
5	✓		NG3 Staging	4 days	03/03/14 08:	06/03/14 05:	4	Kris R, Staging En										
6	✓		NG3 PROD (Web)	4 days	07/03/14 08:	12/03/14 05:	5	Unix, Support										
7	✓		NG3 PROD (feeder)	5 days	13/03/14 08:	19/03/14 05:	6	Unix, Support										
8																		
9			NG3 - 1396	56 days	07/03/14 08:	26/05/14 08:												
10			NG3 Dev	16 days	07/03/14 08:	28/03/14 05:	5	Andrew R, Shilpi,										
11			NG3 testing	4 days	31/03/14 08:	03/04/14 05:	10	Kris R, Test 1 Envi										
12			NG3 Staging	10 days	04/04/14 08:	17/04/14 05:	11	Kris R, Staging En										
13			NG3 PROD (Web)	5 days	18/04/14 08:	24/04/14 05:	12	Unix, Support										
14																		
15			BAU cycle May	0 days	26/05/14 08:	26/05/14 08:												
16			BAU cycle May	0 days	26/05/14 08:	26/05/14 08:	15											
17																		
18			Rural migration (importer)	50 days	22/04/14 08:	30/06/14 05:												
19	✓		Analysis test	3 days	22/04/14 08:	24/04/14 05:	12											
20			Test content creation	5 days	28/04/14 08:	02/05/14 05:	19											
21			Functional testing	10 days	05/05/14 08:	16/05/14 05:	20	Test 1 Environ, Kr										


Project: WCMS BAU RELEASES
Date: 01/03/18 03:18 pm

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	03 Feb '14										10
								S	M	T	W	T	F	S	S	S	M	
22		importer regression	3 days	19/05/14 08:	21/05/14 05:	21	Kris R											
23		Perf testing	5 days	22/05/14 08:	28/05/14 05:	22	Kris R, Staging En											
24		bug fix	3 days	29/05/14 08:	02/06/14 05:	23	Andrew R, Shilpi											
25		Deploy	5 days	03/06/14 08:	09/06/14 05:	24	Unix, Support											
26		Migrate contents	15 days	10/06/14 08:	30/06/14 05:	25	Kris R[10%], Andr											
27		BAU cycle July	0 days	28/07/14 05:	28/07/14 05:	28												
28		BAU cycle July	20 days	01/07/14 08:	28/07/14 05:													
32		BAU cycle AUGUST	20 days	29/07/14 08:	25/08/14 05:													
36		BAU cycle SEPTEMBER	20 days	26/08/14 08:	22/09/14 05:													
40		BAU cycle OCTOBER	0 days	20/10/14 05:	20/10/14 05:	41												
41		BAU cycle OCTOBER	20 days	23/09/14 08:	20/10/14 05:													
45		BAU cycle NOVEMBER	20 days	21/10/14 08:	17/11/14 05:													
49		BAU cycle DECEMBER	20 days	18/11/14 08:	15/12/14 05:													
53		BAU cycle JANUARY	20 days	16/12/14 08:	12/01/15 05:													

Project: WCMS BAU RELEASES
Date: 01/03/18 03:18 pm

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

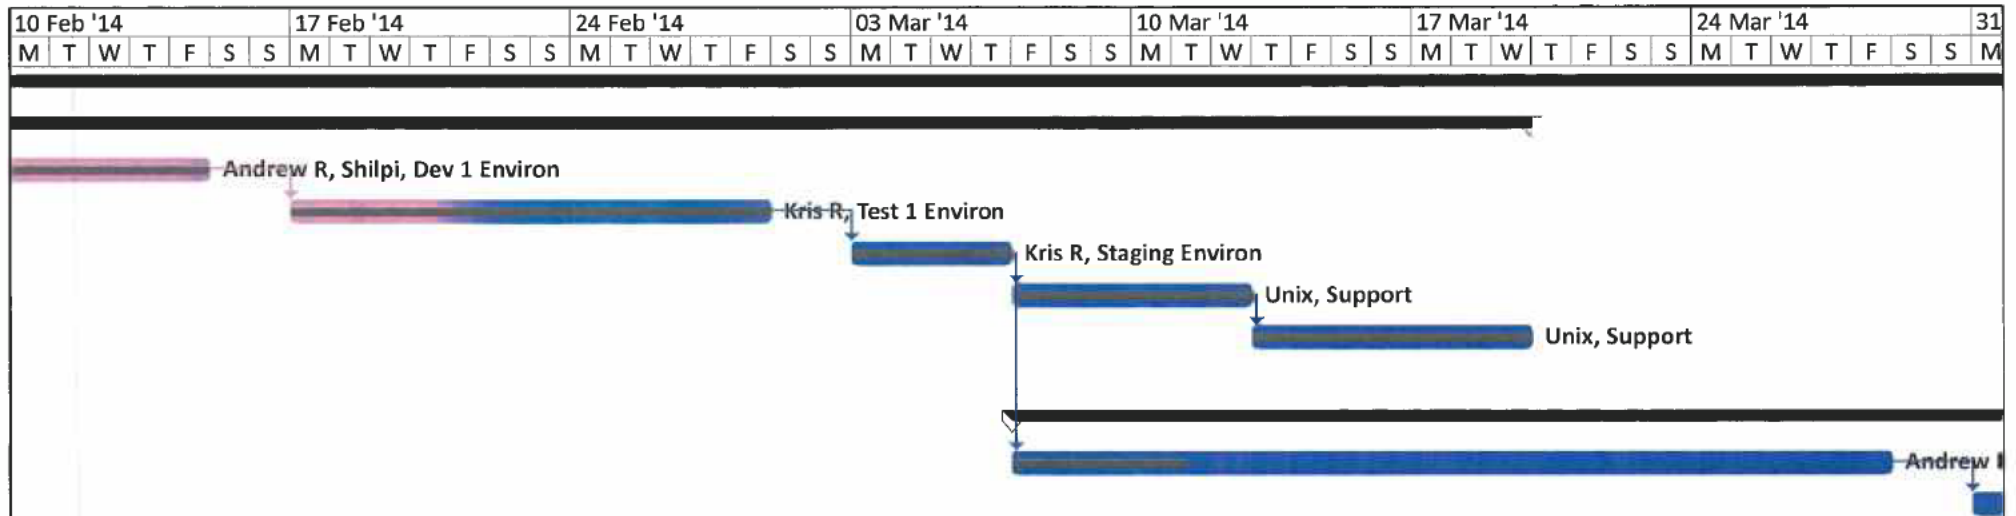

Project: WCMS BAU RELEASES
Date: 01/03/18 03:18 pm

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

[illegible]

31 Mar '14	07 Apr '14	14 Apr '14	21 Apr '14	28 Apr '14	05 May '14	12 May '14	19
M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M

w R, Shilpi, Dev 1 Environ

Kris R, Test 1 Environ

Kris R, Staging Environ

Unix, Support

Test 1 Env

Project: WCMS BAU RELEASES
Date: 01/03/18 03:18 pm

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

Page 6


19 May '14	26 May '14	02 Jun '14	09 Jun '14	16 Jun '14	23 Jun '14	30 Jun '14	07
M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M T W T F S S	M

◇ 26/05

◇ 26/05

Environ, Kris R

Project: WCMS BAU RELEASES Date: 01/03/18 03:18 pm	Task		External Milestone	◇	Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone	◇	Inactive Milestone	◇	Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	↓
	External Tasks		Duration-only		Progress	

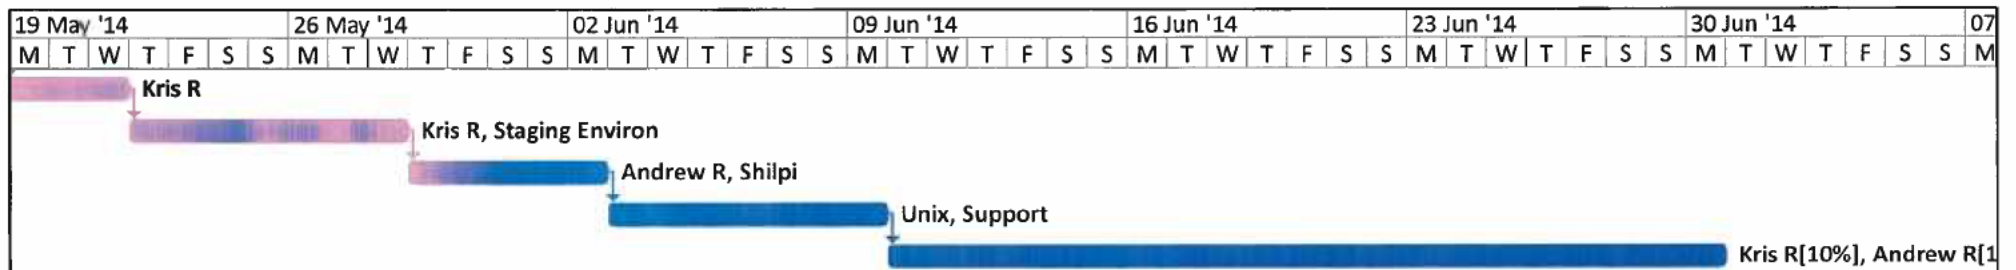


Project: WCMS BAU RELEASES Date: 01/03/18 03:18 pm	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	


07 Jul '14							14 Jul '14							21 Jul '14							28 Jul '14							04 Aug '14							11 Aug '14							18 Aug '14							25
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

Project: WCMS BAU RELEASES
Date: 01/03/18 03:18 pm


Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

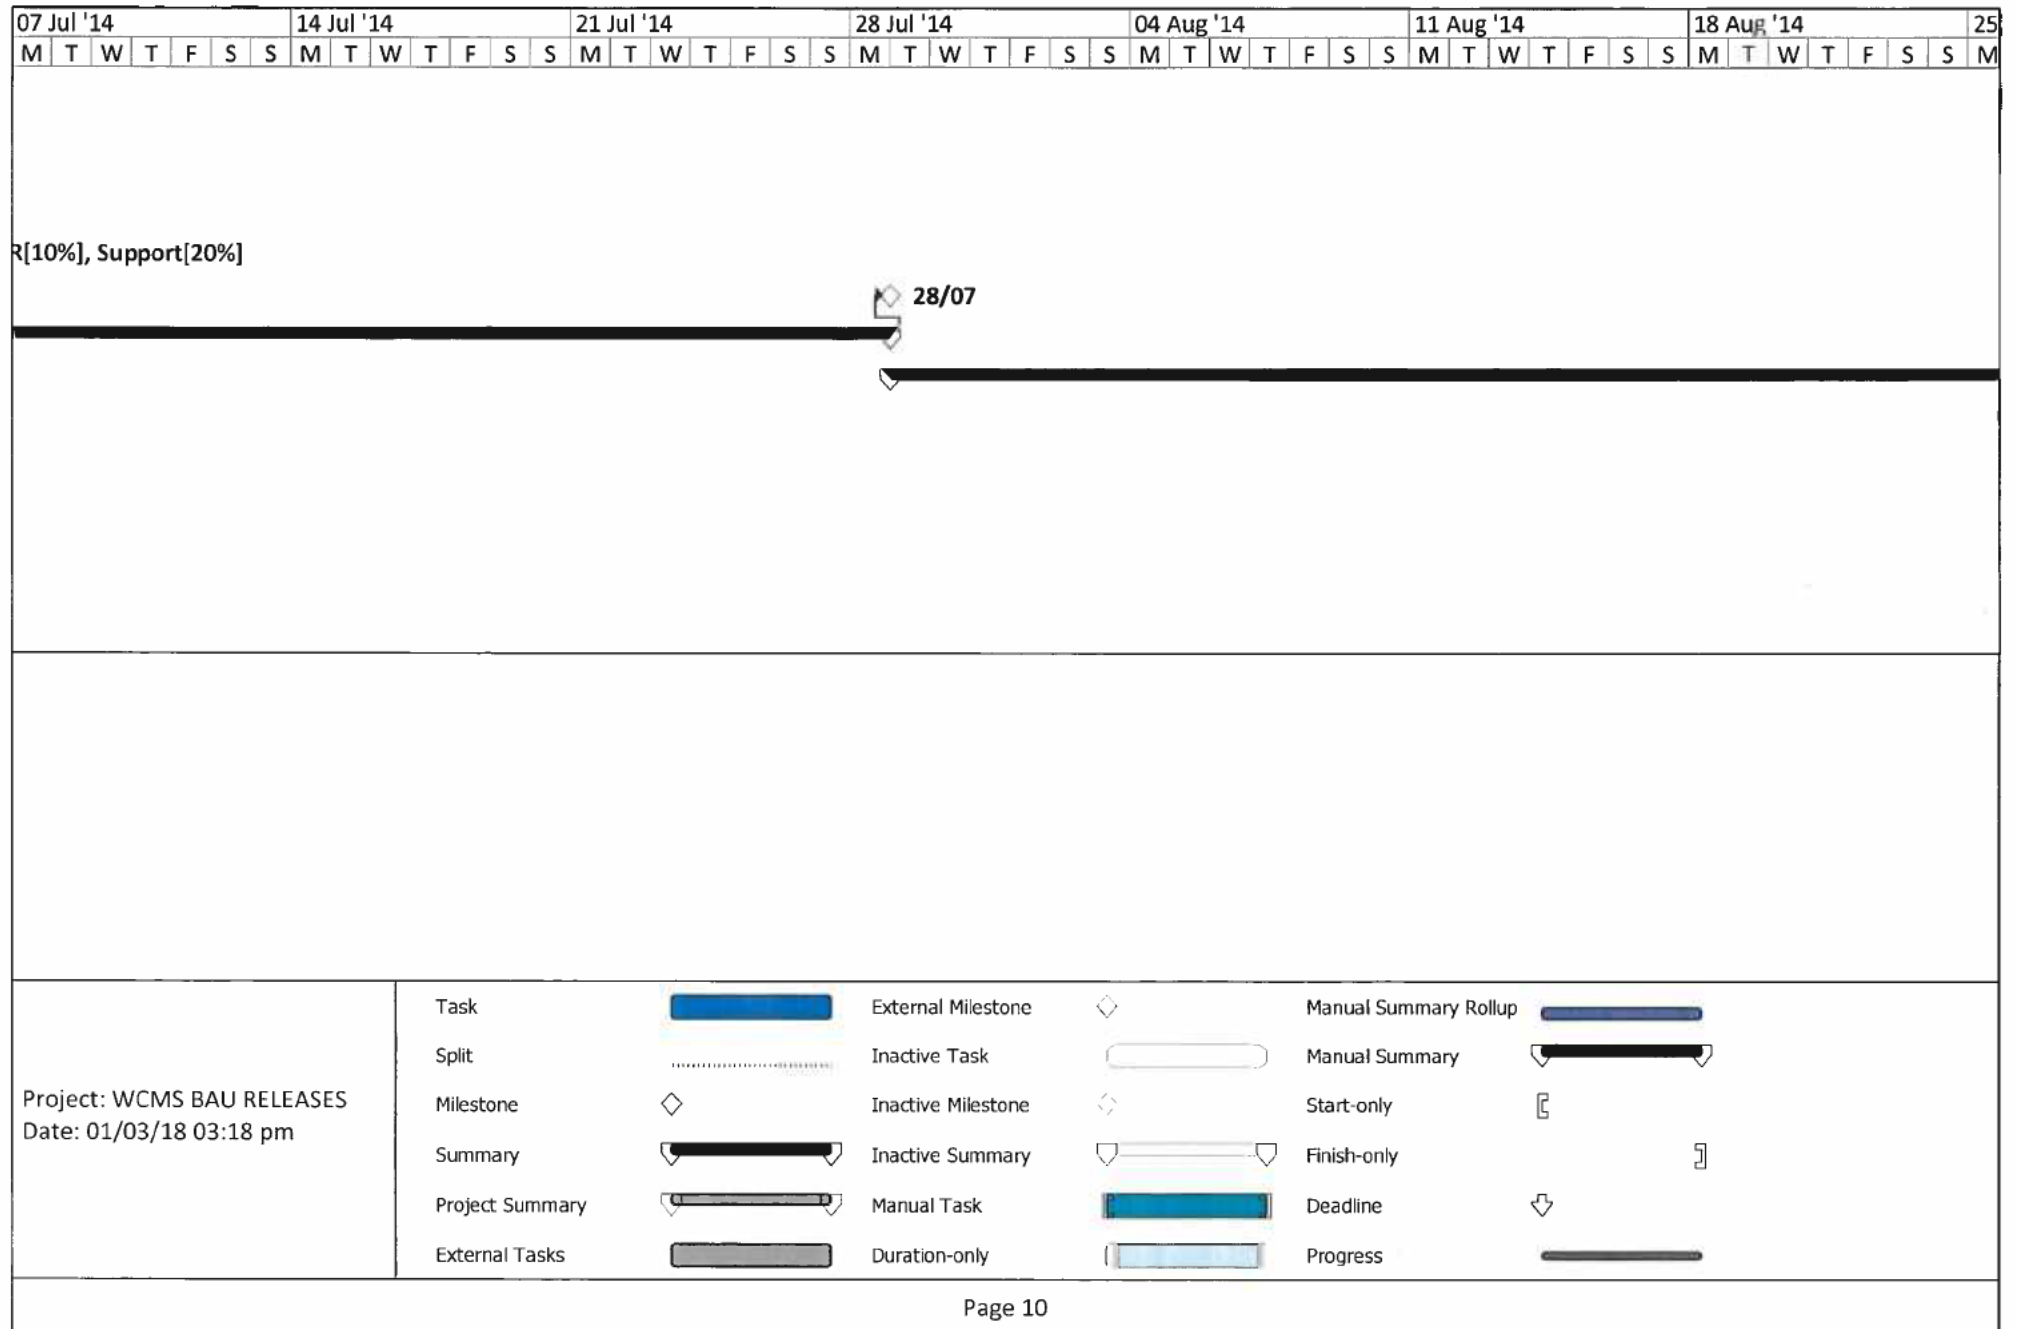


25 Aug '14							01 Sep '14							08 Sep '14							15 Sep '14							22 Sep '14							29 Sep '14							06 Oct '14							13
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

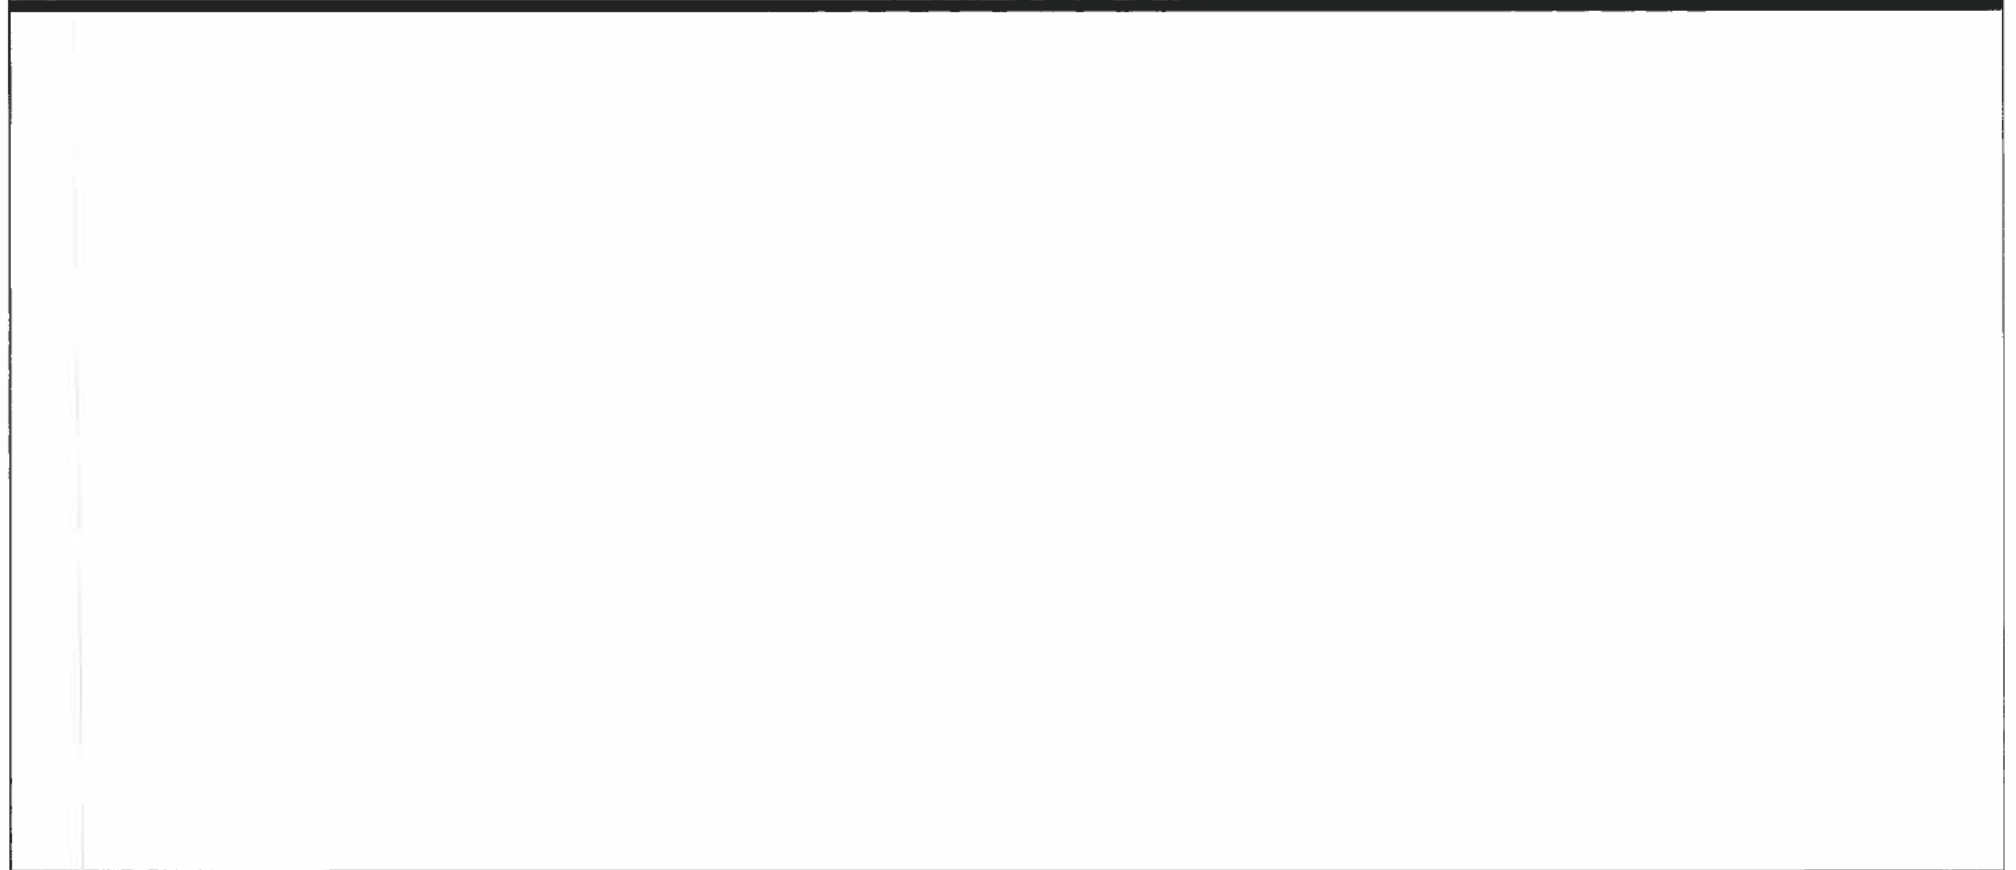


Project: WCMS BAU RELEASES Date: 01/03/18 03:18 pm	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

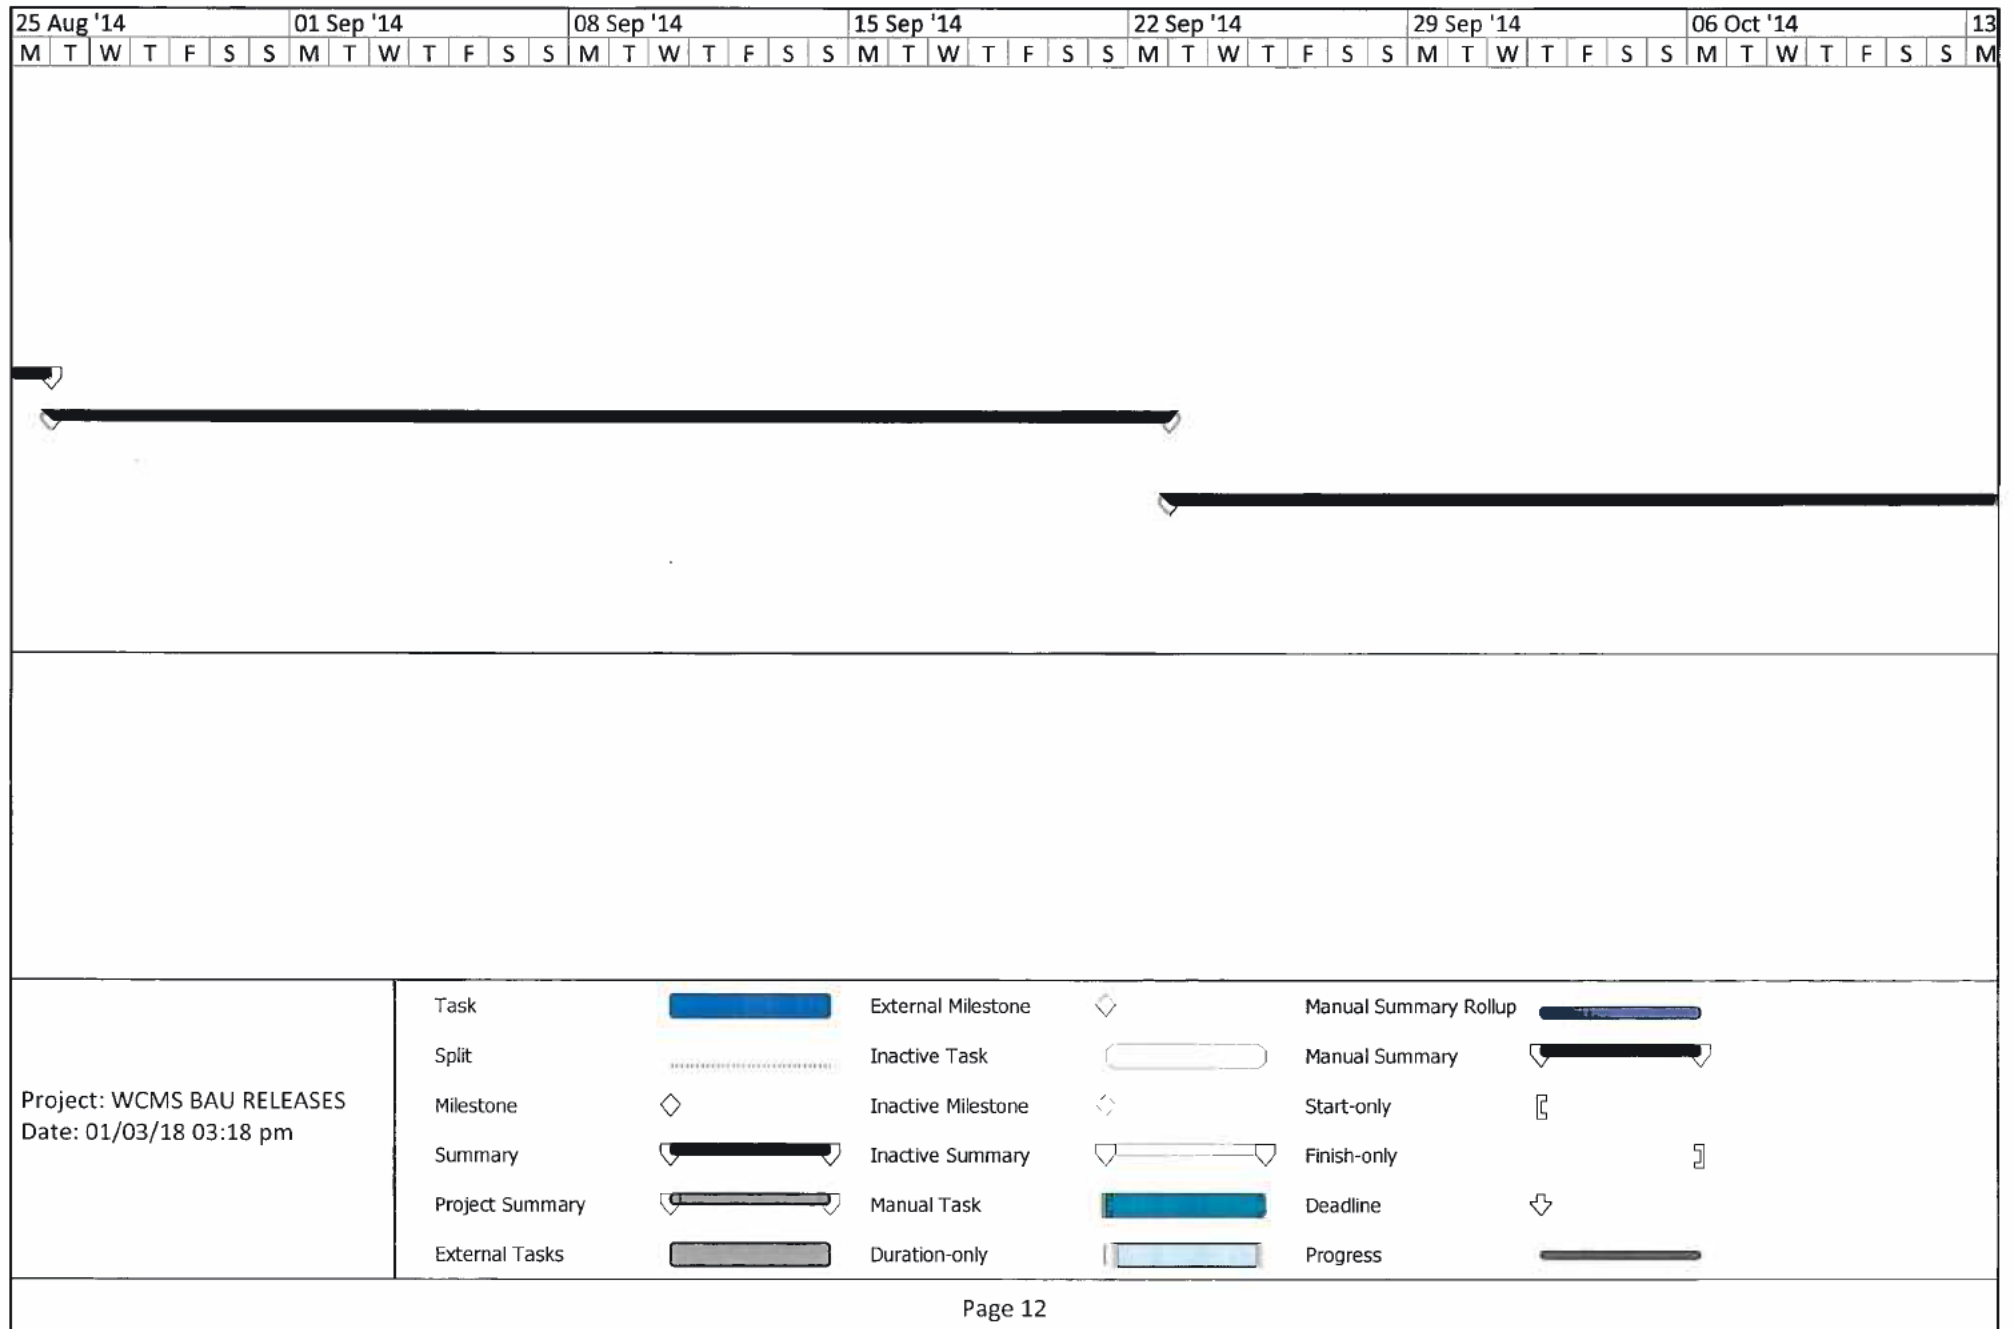

13 Oct '14							20 Oct '14							27 Oct '14							03 Nov '14							10 Nov '14							17 Nov '14							24 Nov '14							01
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M




Project: WCMS BAU RELEASES Date: 01/03/18 03:18 pm	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

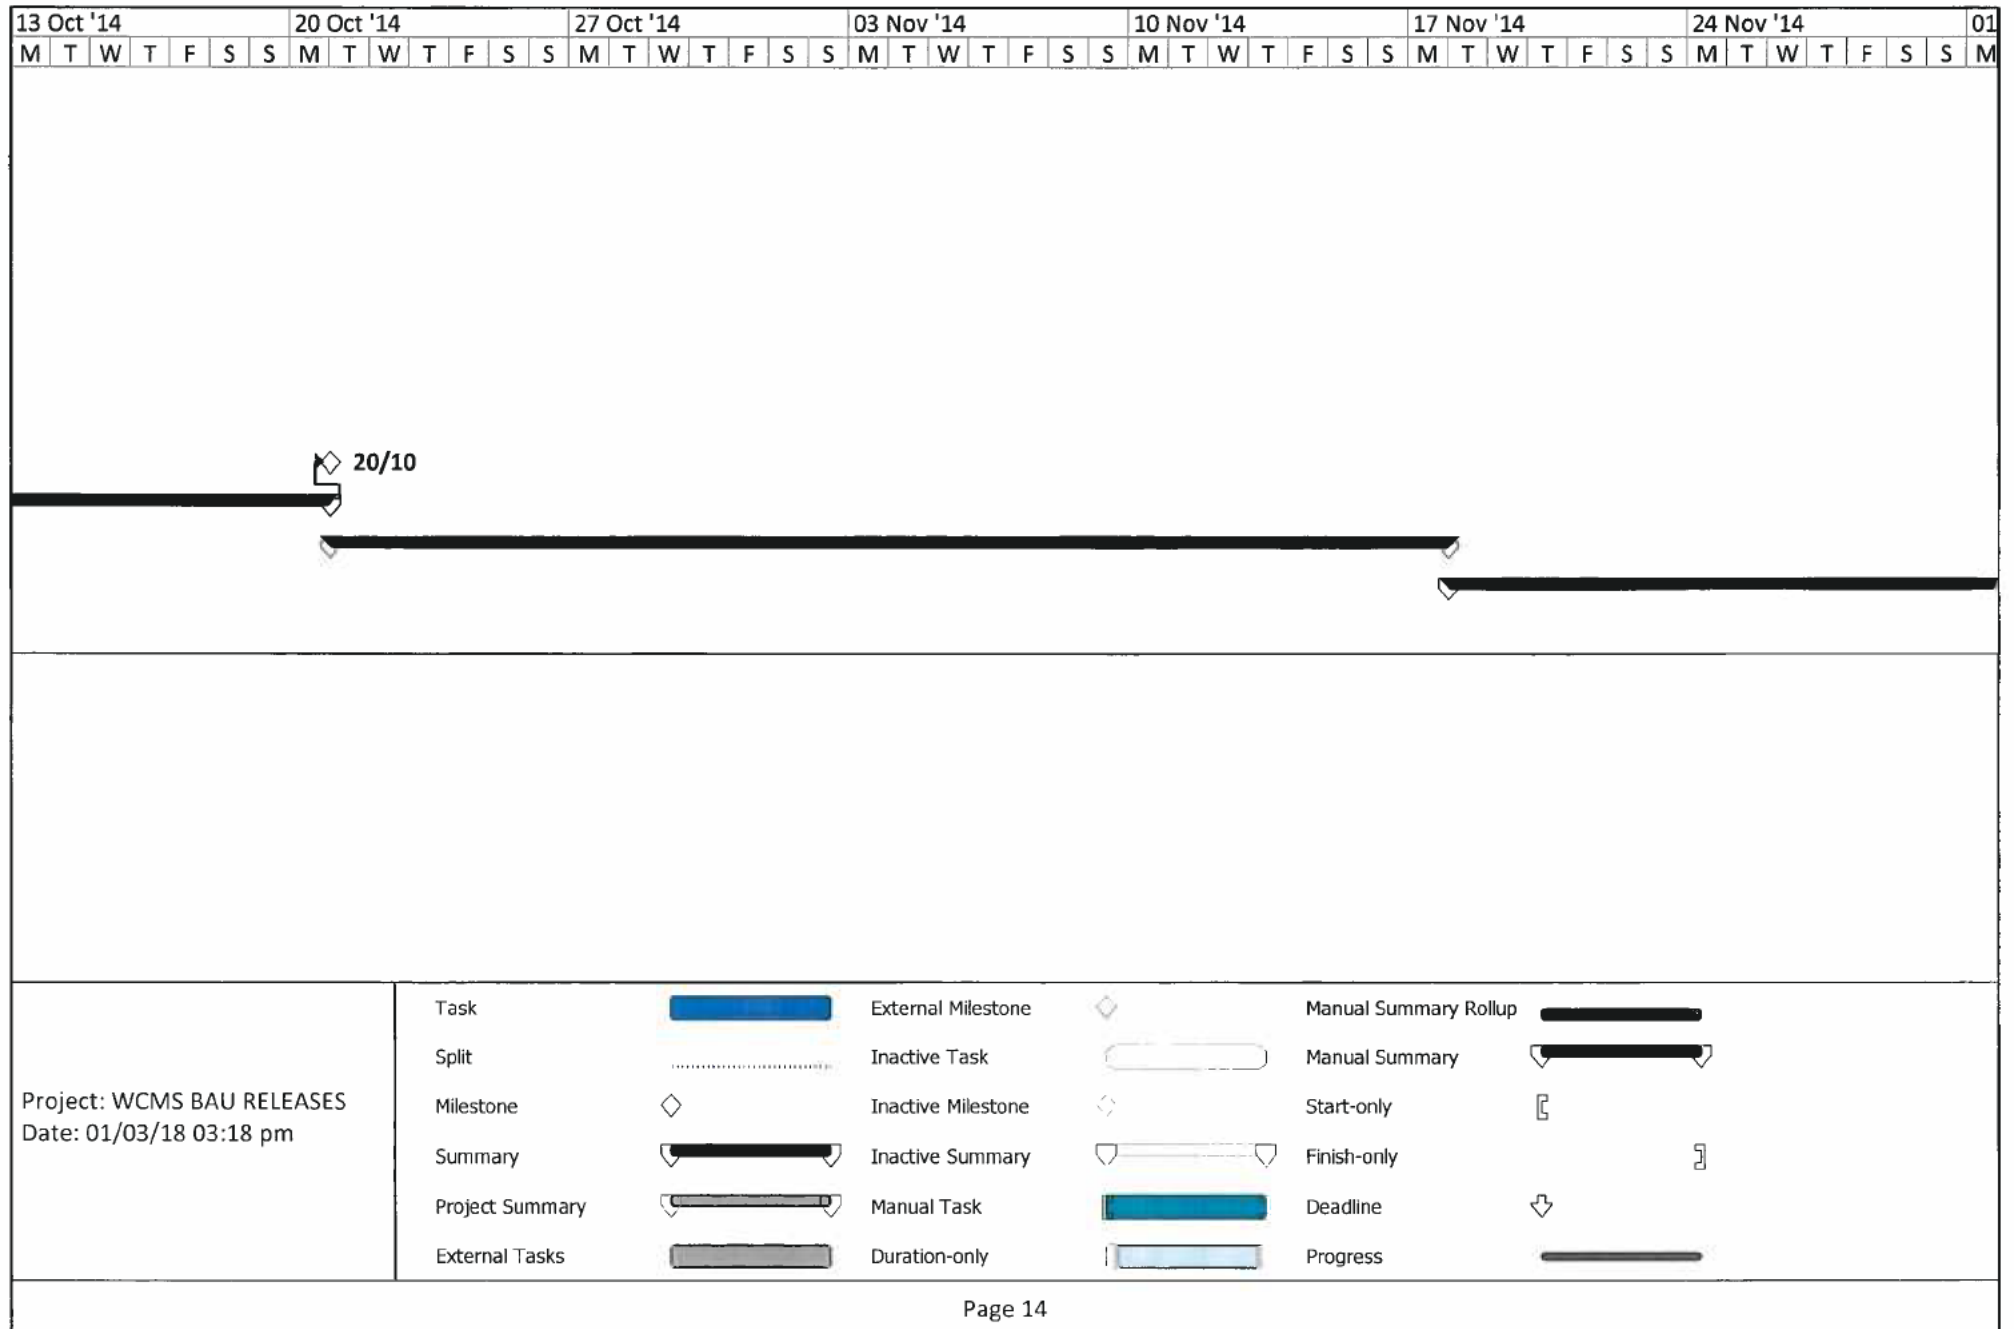

[illegible]Page 15

01 Dec '14							08 Dec '14							15 Dec '14							22 Dec '14							29 Dec '14							05 Jan '15							12 Jan '15							19
M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M

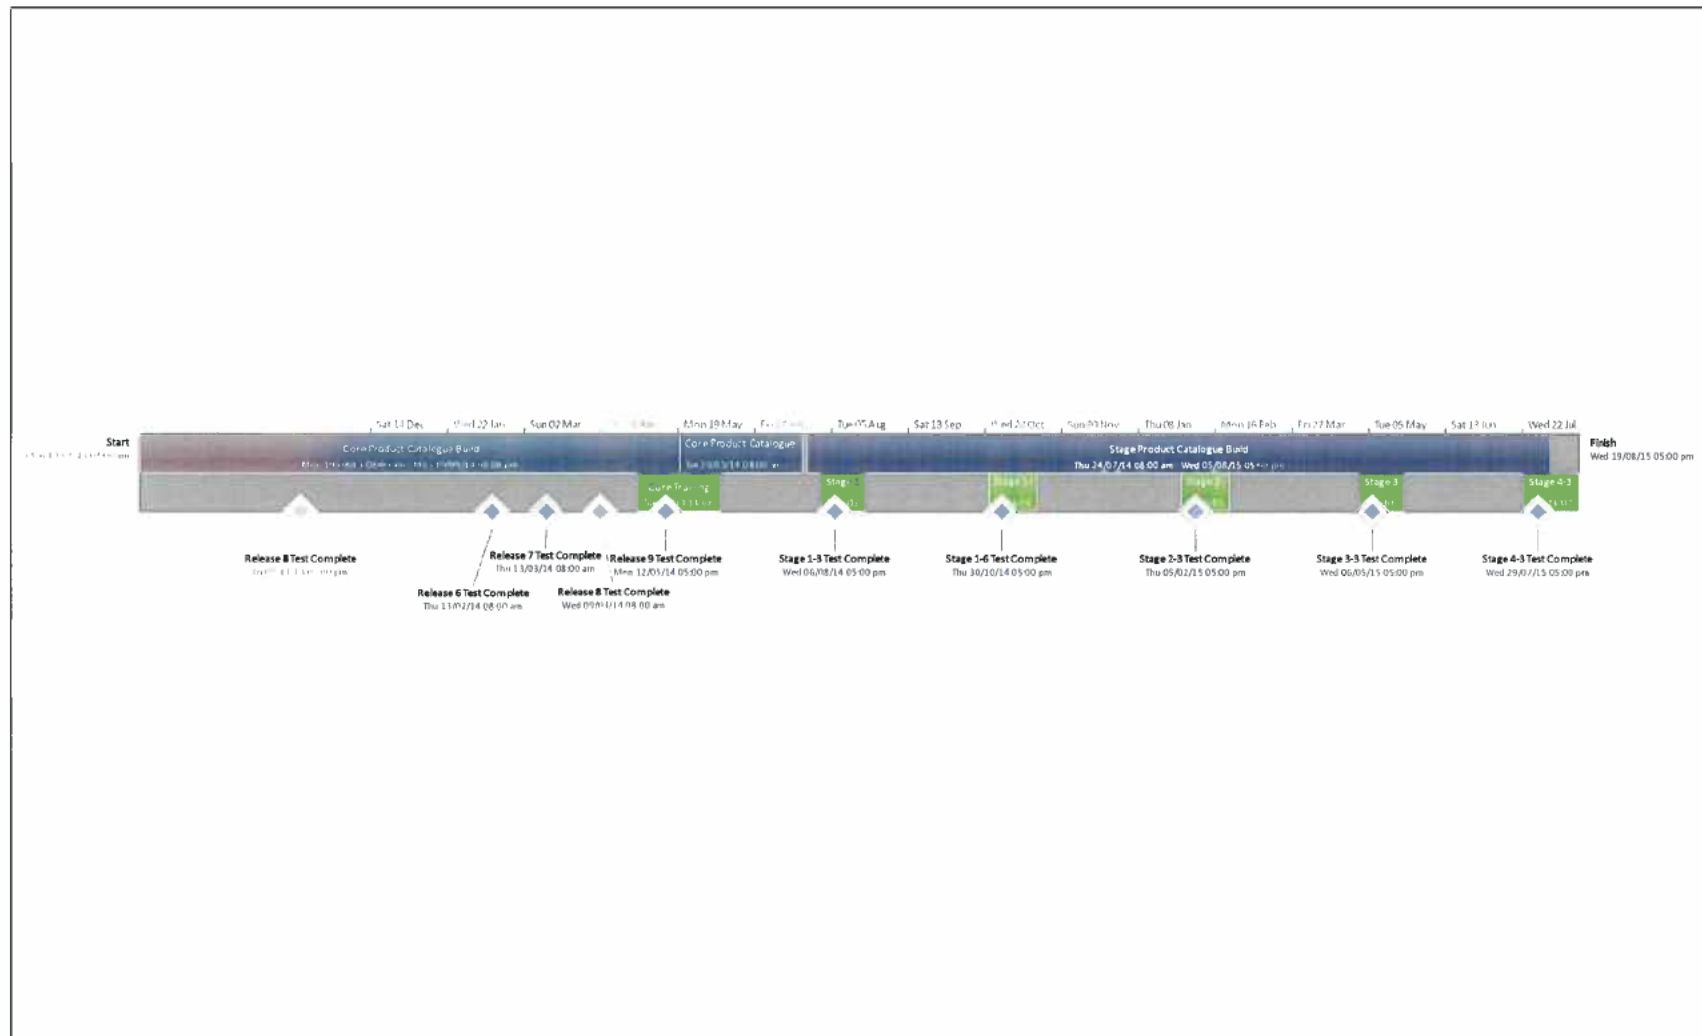

ID	Task Name	Duration	% Complete	Start	Finish	Resource Names	Predecessors	Work	Actual Work	Remaining Work	% Work Completed	Planned Release	Expected Release
0	WCMS Feature Build Schedule	568 days	39%	01/05/13 08:00	29/07/15 05:00			6531 days	2737.56 days	3793.43 days	42%		
1													
2	Design	511 days	41%	06/05/13 08:00	13/05/15 05:00			2538 days	1120 days	1418 days	44%		
3	design CORE	241 days	99%	06/05/13 08:00	14/04/14 05:00			1038 days	1038 days	0 days	100%		
172	design STAGE 1 NEWS & INFORMATION	136 days	12%	03/02/14 08:00 am	15/08/14 05:00 pm			600 days	82 days	518 days	14%		
173	Design Release Stage 1 -1	40 days	43%	03/02/14 08:00	28/03/14 05:00			100 days	48 days	52 days	48%	10	10
188	Design Release Stage 1 -2	41 days	8%	25/02/14 08:00	24/04/14 05:00			100 days	9 days	91 days	9%	11	11
203	Design Release Stage 1 -3	42 days	12%	31/03/14 08:00	30/05/14 05:00			100 days	15 days	85 days	15%	12	12
219	Design Release Stage 1 -4	39 days	2%	28/04/14 08:00	20/06/14 05:00			100 days	2 days	98 days	2%	13	13
235	Design Release Stage 1 -5	39 days	8%	02/06/14 08:00	25/07/14 05:00			100 days	8 days	92 days	8%	14	14
253	Design Release Stage 1-6	40 days	0%	23/06/14 08:00	15/08/14 05:00			100 days	0 days	100 days	0%	15	15
272	Gap Analysis RADIO	35 days	0%	06/06/14 08:00	25/07/14 05:00			0 days	0 days	0 days	0%		
276	design STAGE 2 RADIO	80 days	0%	28/07/14 08:00	17/11/14 05:00			300 days	0 days	300 days	0%		
341	design STAGE 3 TV	80 days	0%	14/10/14 08:00	09/02/15 05:00			300 days	0 days	300 days	0%		
396	design STAGE 4 OTHER	80 days	0%	19/01/15 08:00	13/05/15 05:00			300 days	0 days	300 days	0%		
437	Build	525 days	44%	12/06/13 08:00	10/07/15 05:00			3993 days	1617.56 days	2375.43 days	41%		
438	build CORE	217 days	93%	12/06/13 08:00	17/04/14 05:00			1608 days	1580.56 days	27.44 days	98%		
564	build STAGE 1 NEWS & INFORMATION	121 days	2%	22/04/14 08:00 am	10/10/14 05:00 pm			1114 days	15 days	1099 days	1%		
565	Build release S1-1	23 days	0%	22/04/14 08:00	23/05/14 05:00			204 days	0 days	204 days	0%	10	10
574	Build release S1-2	19 days	0%	26/05/14 08:00	20/06/14 05:00			210 days	0 days	210 days	0%	11	11
583	Build release S1-3	20 days	13%	23/06/14 08:00	18/07/14 05:00			205 days	15 days	190 days	7%	12	12
598	Build release S1-4	20 days	0%	21/07/14 08:00	15/08/14 05:00			200 days	0 days	200 days	0%	13	13
608	Build release S1-5	20 days	0%	18/08/14 08:00	12/09/14 05:00			193 days	0 days	193 days	0%	14	14
620	Build release S1-6	19 days	0%	15/09/14 08:00	10/10/14 05:00			102 days	0 days	102 days	0%	15	15
633	build STAGE 2 RADIO	66 days	0%	13/10/14 08:00	16/01/15 05:00			564 days	0 days	564 days	0%		
676	build STAGE 3 TV	62 days	0%	19/01/15 08:00	17/04/15 05:00			372 days	22 days	350 days	6%		
709	build STAGE 4 OTHER	59 days	0%	20/04/15 08:00	10/07/15 05:00			335 days	0 days	335 days	0%		
732	Test	568 days	0%	01/05/13 08:00	29/07/15 05:00			0 days	0 days	0 days	0%		
733	test CORE	261 days	0%	01/05/13 08:00	12/05/14 05:00			0 days	0 days	0 days	0%		

Project: WCMS Feature Build Schedule
Date: 01/03/18 03:19 pm

Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary		Manual Progress	
Project Summary		Inactive Summary		Start-only			

ID	Task Name	Duration	% Complete	Start	Finish	Resource Names	Predecessors	Work	Actual Work	Remaining Work	% Work Completed	Planned Release	Expected Release
733	test CORE	261 days	0%	01/05/13 08	12/05/14 05:00			0 days	0 days	0 days	0%		
839	test STAGE 1 NEWS & INFORMATION	135 days	0%	22/04/14 08:00 am	30/10/14 05:00 pm			0 days	0 days	0 days	0%		
840	Test Release Stage 1-1	36 days	0%	22/04/14 08	12/06/14 05:00			0 days	0 days	0 days	0%	11	11
856	Test Release Stage 1-2	33 days	0%	26/05/14 08	10/07/14 05:00			0 days	0 days	0 days	0%	12	12
872	Test Release Stage 1-3	33 days	0%	23/06/14 08	06/08/14 05:00			0 days	0 days	0 days	0%	13	13
893	Test Release Stage 1-4	33 days	0%	21/07/14 08	03/09/14 05:00			0 days	0 days	0 days	0%	14	14
909	Test Release Stage 1-5	33 days	0%	18/08/14 08	01/10/14 05:00			0 days	0 days	0 days	0%	15	15
925	Test Release Stage 1-6	33 days	0%	15/09/14 08	30/10/14 05:00			0 days	0 days	0 days	0%	15	15
946	test STAGE 2 RADIO	79 days	0%	13/10/14 08	05/02/15 05:00			0 days	0 days	0 days	0%		
1000	test Stage 3 TV	75 days	0%	19/01/15 08	06/05/15 05:00			0 days	0 days	0 days	0%		
1054	test STAGE 4 OTHER	72 days	0%	20/04/15 08	29/07/15 05:00			0 days	0 days	0 days	0%		

Project: WCMS Feature Build Schedule
Date: 01/03/18 03:19 pm

Task		External Tasks		Manual Task		Finish-only	
Split		External Milestone		Duration-only		Deadline	
Milestone		Inactive Task		Manual Summary Rollup		Progress	
Summary		Inactive Milestone		Manual Summary		Manual Progress	
Project Summary		Inactive Summary		Start-only			

Actual Duration	Feature Number	M																B								E								M															
		01 Apr '13				08 Apr '13				15 Apr '13				22 Apr '13				29 Apr '13				06 May '13				13 May '13				20 May '13				27 May '13				03 Jun '13				10 Jun '13				17 Jun '13			
		31	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30	01	03	05	07	09	11	13	15	17	19	21						
223.25 days																																																	
210.01 days																																																	
239.77 days																																																	
15.94 days																																																	
17.12 days																																																	
3.3 days																																																	
4.97 days																																																	
0.92 days																																																	
2.98 days																																																	
0 days																																																	
0 days																																																	
0 days																																																	
0 days																																																	
0 days																																																	
229.03 days																																																	
201.65 days																																																	
2.61 days																																																	
0 days																																																	
0 days																																																	
2.5 days																																																	
0 days																																																	
0 days																																																	
0 days																																																	
0 days																																																	
0.13 days																																																	
0 days																																																	
0 days																																																	
0 days																																																	

Project: WCMS Feature Build Schedule

Date: 01/03/18 03:19 pm

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only

Finish-only

Deadline

Progress

Manual Progress

Page 3

Project: WCMS Feature Build Schedule Date: 01/03/18 03:19 pm	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary		Manual Progress	
	Project Summary		Inactive Summary		Start-only			

E					M					B					E					M																																																	
24 Jun '13					01 Jul '13					08 Jul '13					15 Jul '13					22 Jul '13					29 Jul '13					05 Aug '13					12 Aug '13					19 Aug '13					26 Aug '13					02 Sep '13					09 Sep '13					16 Sep '13					23 Sep '13				
21	23	25	27	29	01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30	01	03	05	07	09	11	13	15	17	19	21	23	25	27																				

Project: WCMS Feature Build Schedule
Date: 01/03/18 03:19 pm

Task



External Tasks



Manual Task



Finish-only



Split



External Milestone



Duration-only



Deadline



Milestone



Inactive Task

Manual Summary Rollup



Progress



Summary



Inactive Milestone

Manual Summary



Manual Progress



Project Summary



Inactive Summary

Start-only



[illegible]Page 6


[illegible]

[illegible]


Project: WCMS Feature Build Schedule Date: 01/03/18 03:19 pm	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary		Manual Progress	
	Project Summary		Inactive Summary		Start-only			
Page 8								

[illegible]

E												M												B												E												M									
06 Jan '14					13 Jan '14				20 Jan '14				27 Jan '14				03 Feb '14				10 Feb '14				17 Feb '14				24 Feb '14				03 Mar '14				10 Mar '14				17 Mar '14				24 Mar '14				31 Mar '14				07 Apr '14				
03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	02	04	06	08	10	12	14	16	18	20	22	24	26	28	02	04	06	08	10	12	14	16	18	20	22	24	26	28	30	01	03	05	07	09	11								

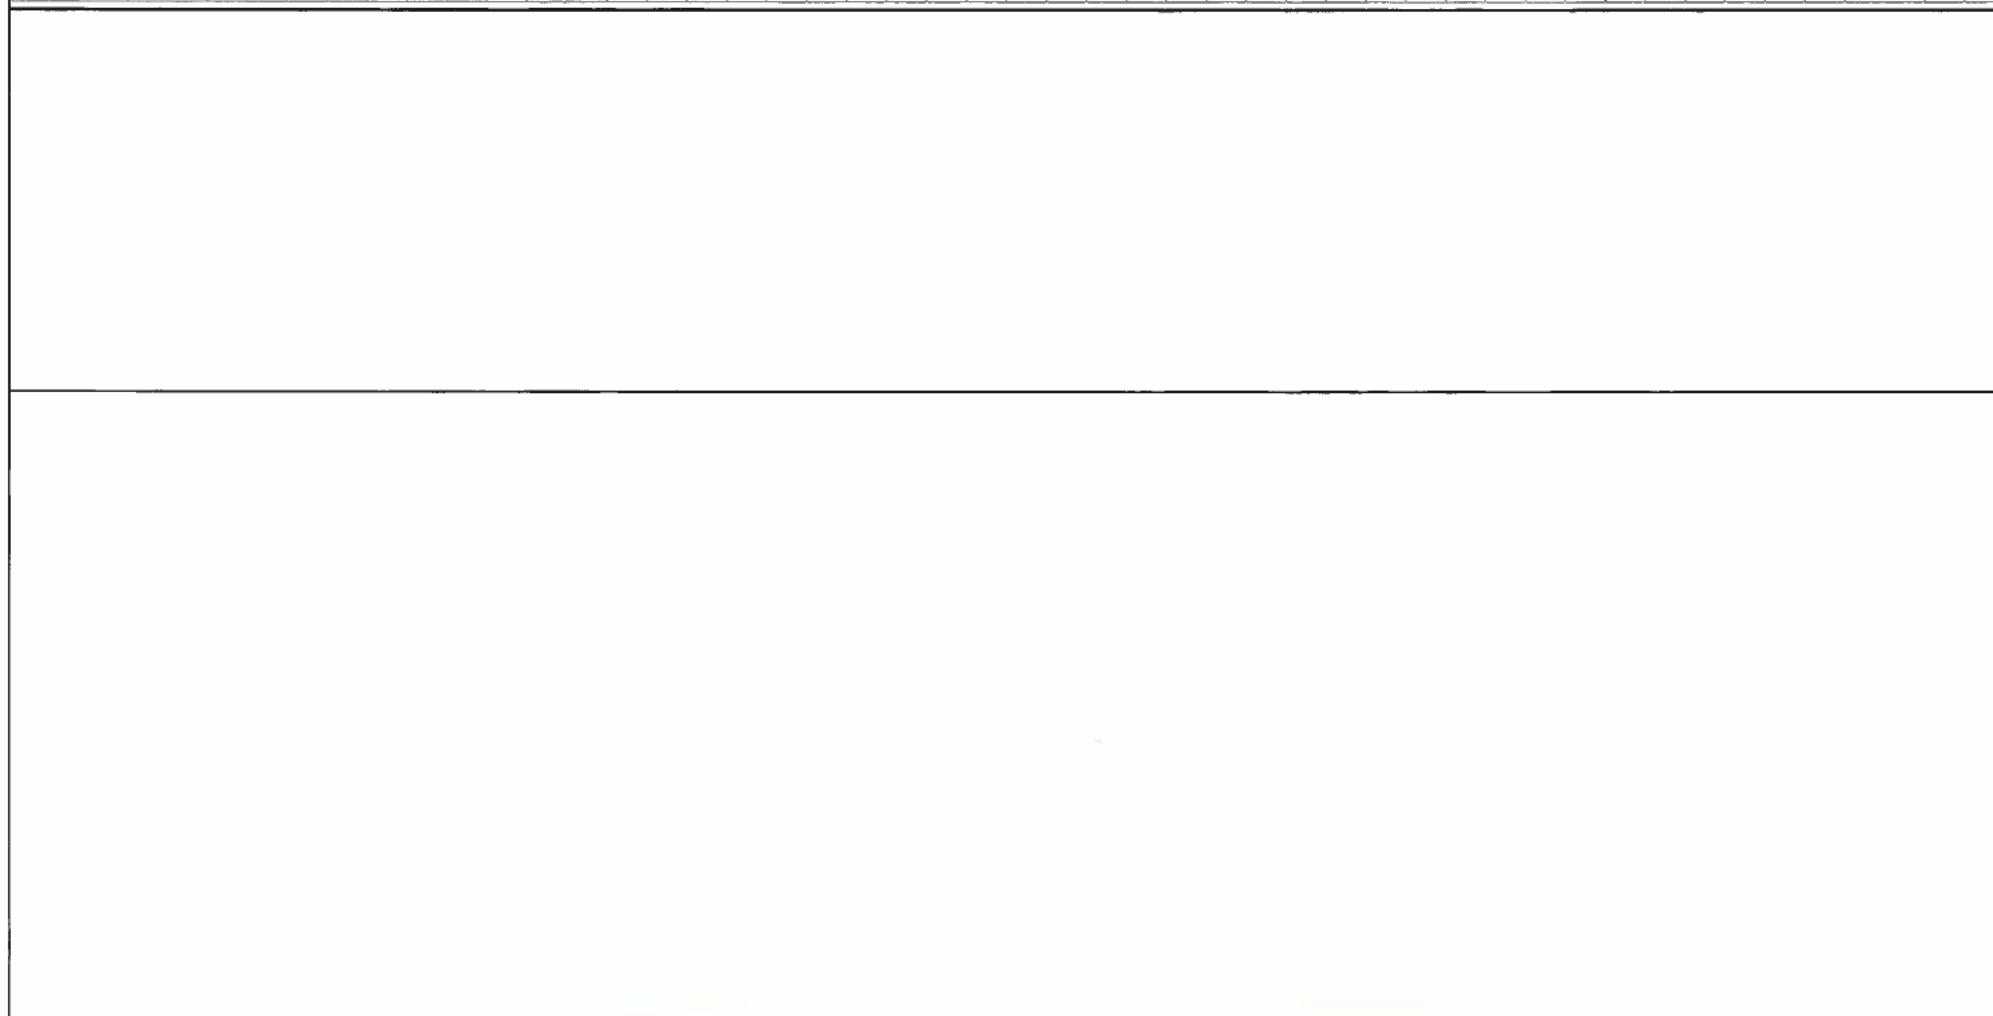


Project: WCMS Feature Build Schedule Date: 01/03/18 03:19 pm	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary		Manual Progress	
	Project Summary		Inactive Summary		Start-only			

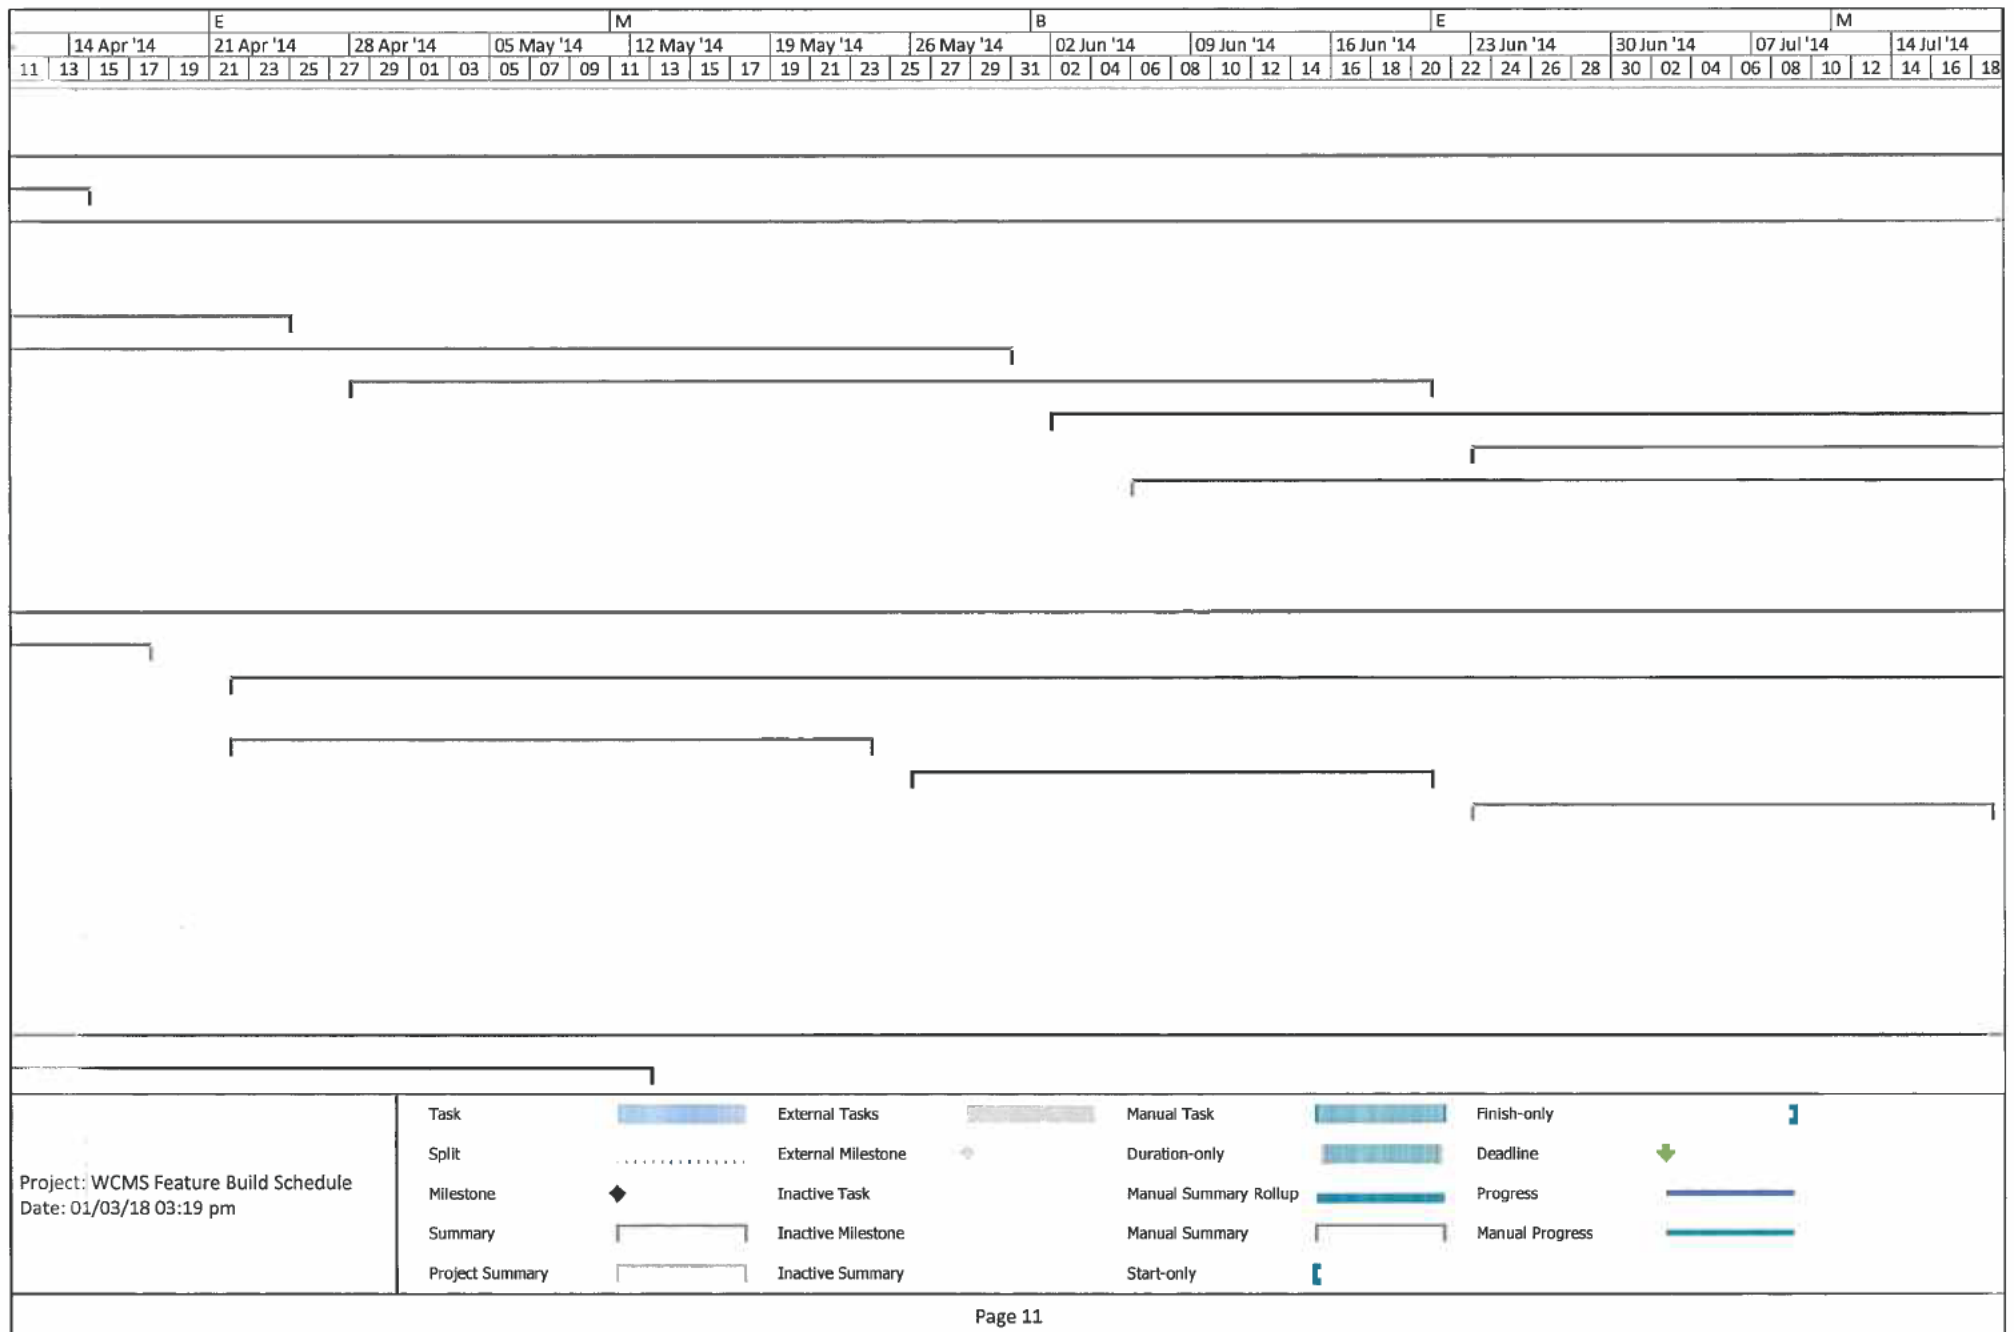



[illegible]

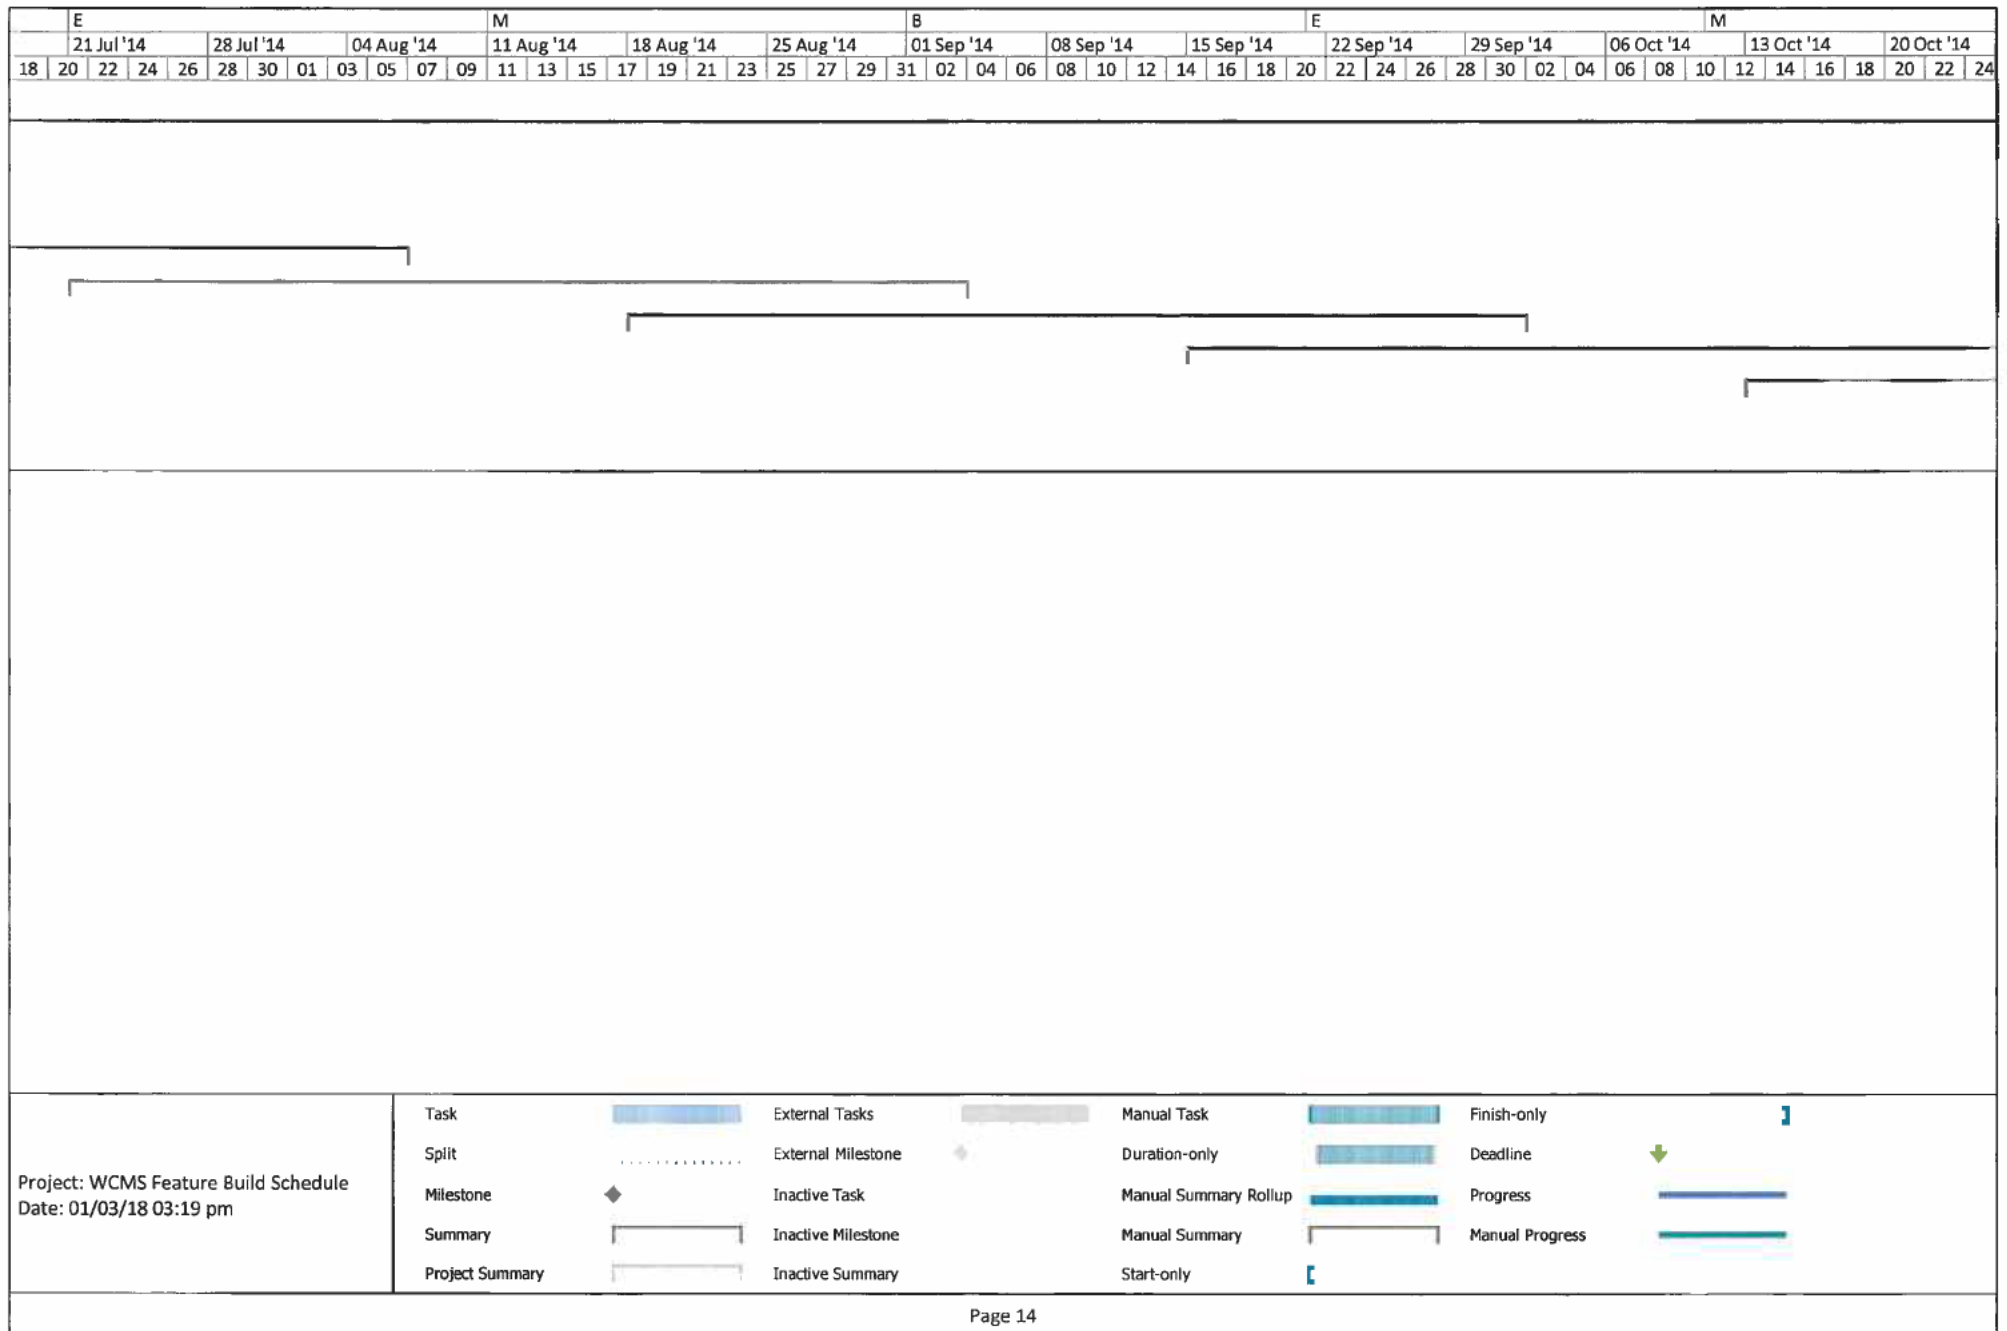


[illegible]

[illegible]


[illegible]Page 17

[illegible]

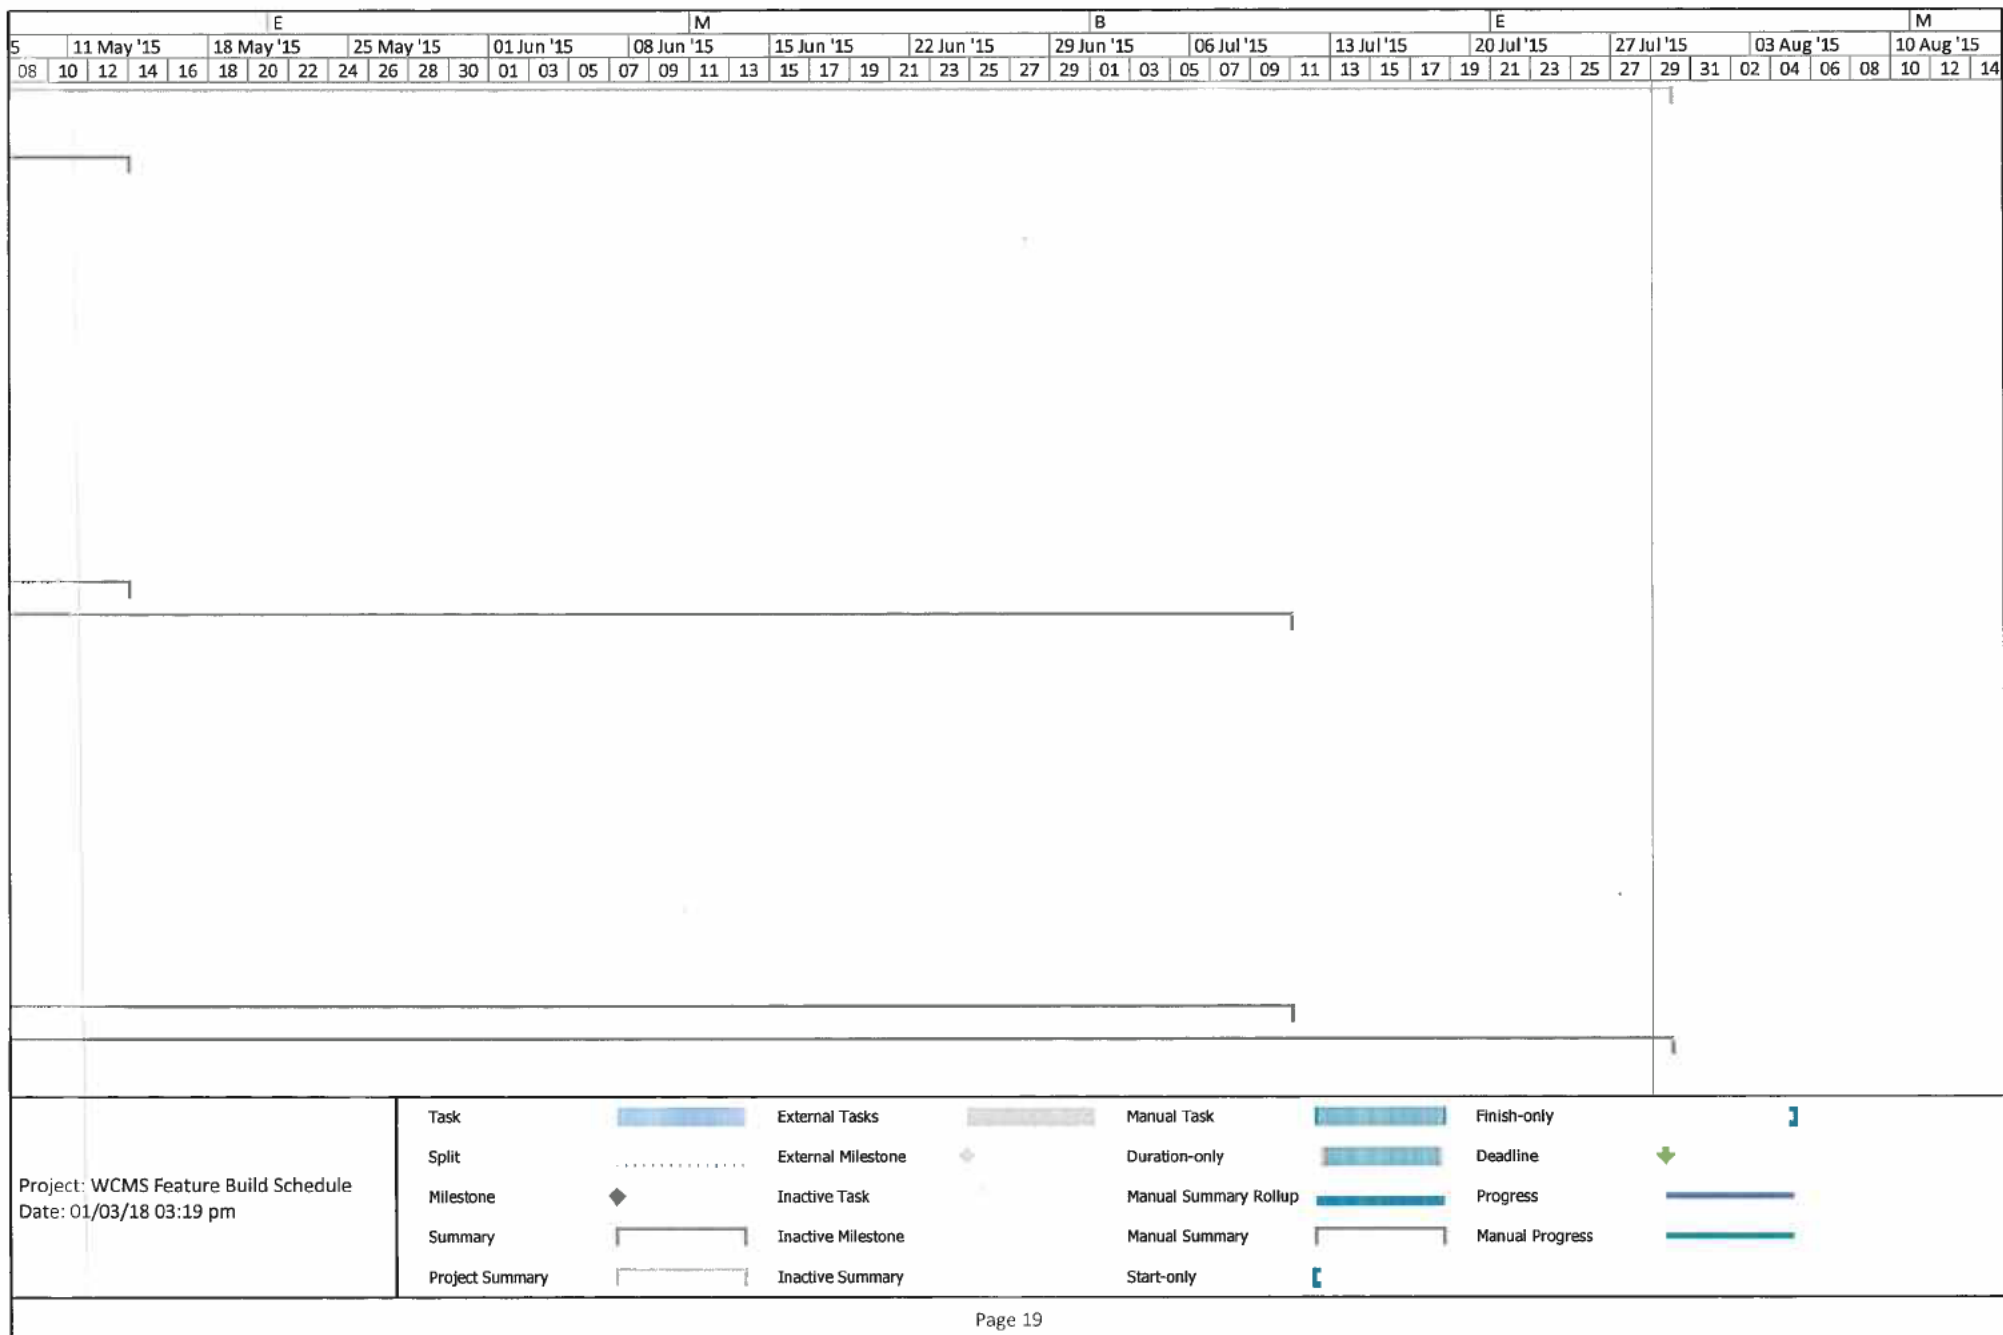

E										M				B				E				M																																															
11 May '15					18 May '15					25 May '15					01 Jun '15					08 Jun '15					15 Jun '15					22 Jun '15					29 Jun '15					06 Jul '15					13 Jul '15					20 Jul '15					27 Jul '15					03 Aug '15					10 Aug '15				
08	10	12	14	16	18	20	22	24	26	28	30	01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	01	03	05	07	09	11	13	15	17	19	21	23	25	27	29	31	02	04	06	08	10	12	14																				

ID	Task Name	Duration	% Complete	Start	Finish	Resource Names	Predecessors	Work	Actual Work	Remaining Work	% Work Complete	Planned Release	Expected Release	May 2013							March 2015																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																										
														1 May			1 April				1 March			1	1 March			1																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			
														28/01	08/07	16/12	26/05	03/11	13/04	21/09	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21

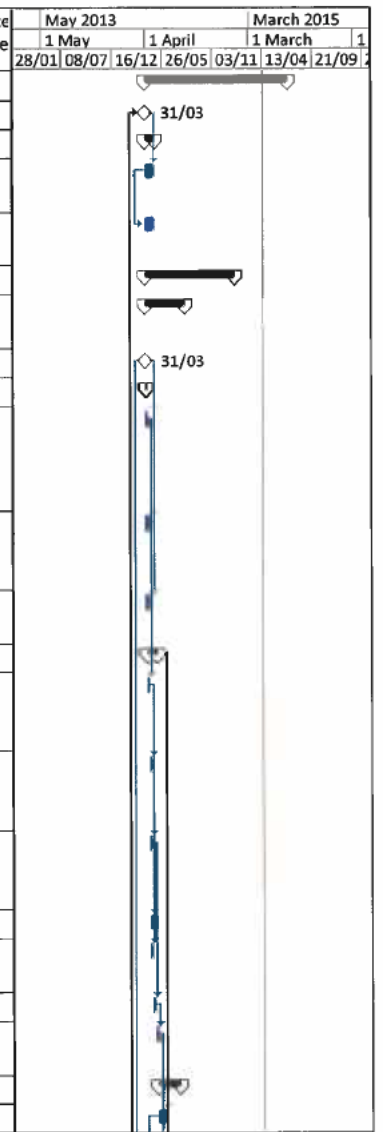

Project: WCMS Integration Schedule
Date: 01/03/18 03:22 pm

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	% Complete	Start	Finish	Resource Names	Predecessor	Work	Actual Work	Remaining Work	% Work Complete	Planned Release	Expected Release	May 2013		April		March 2015	
														1 May	16/12	26/05	03/11	13/04	21/09
22	Regression testing analysis	10 days	0%	08/05/14 08:00 am	21/05/14 05:00 pm		12	0 days	0 days	0 days	0%								
23	Regression testing	20 days	0%	22/05/14 08	19/06/14 05:00		22	0 days	0 days	0 days	0%								
24	Error Correction	20 days	0%	08/05/14 08	04/06/14 05:00		21SS	0 days	0 days	0 days	0%								
25	Performance testing	15 days	0%	22/05/14 08	12/06/14 05:00		24FS-10	0 days	0 days	0 days	0%								
26	Performance tuning	5 days	0%	13/06/14 08	19/06/14 05:00		25	0 days	0 days	0 days	0%								
27	Error Correction	5 days	0%	20/06/14 08	26/06/14 05:00		23, 26	0 days	0 days	0 days	0%								
28	User Acceptance Testing (UAT)	15 days	0%	27/06/14 08:00 am	17/07/14 05:00 pm		23, 27	0 days	0 days	0 days	0%								
29	Deploy	5 days	0%	29/07/14 08	04/08/14 05:00			0 days	0 days	0 days	0%								
30	BAU cycle July	0 days	0%	28/07/14 05	28/07/14 05:00			0 days	0 days	0 days	0%								
31	Deploy to Production	5 days	0%	29/07/14 08	04/08/14 05:00		28, d:\s	0 days	0 days	0 days	0%								
32	NEWS & RADIO NATIONAL RESS support - COMPLETE	0 days	0%	04/08/14 05:00 pm	04/08/14 05:00 pm		31	0 days	0 days	0 days	0%								
33	RESS Support - COMPLETE	0 days	0%	04/08/14 05	04/08/14 05:00		32	0 days	0 days	0 days	0%								
34	Part B (Task 2) RESS Support - COMPLETE	0 days	0%	22/10/14 05:00 pm	22/10/14 05:00 pm		32	0 days	0 days	0 days	0%								
35	Backport Phase 2 (Continuous)	146 days	0%	31/03/14 08	27/10/14 05:00			0 days	0 days	0 days	0%								
36	Analysis	50 days	0%	31/03/14 08	12/06/14 05:00		7SS	0 days	0 days	0 days	0%								
37	Build	48 days	0%	15/05/14 08	22/07/14 05:00			0 days	0 days	0 days	0%								
38	Port of Phase 2	48 days	0%	15/05/14 08	22/07/14 05:00		36FS-20	0 days	0 days	0 days	0%								
39	Testing	50 days	0%	16/07/14 08	23/09/14 05:00			0 days	0 days	0 days	0%								
40	Automation Tests	48 days	0%	08/05/14 08	15/07/14 05:00		36SS, 1	0 days	0 days	0 days	0%								
41	Regression testing analysis	10 days	0%	23/07/14 08:00 am	05/08/14 05:00 pm		38	0 days	0 days	0 days	0%								
42	Regression testing	20 days	0%	06/08/14 08	02/09/14 05:00		41	0 days	0 days	0 days	0%								
43	Error Correction	20 days	0%	16/07/14 08	12/08/14 05:00		40SS	0 days	0 days	0 days	0%								
44	Performance testing	15 days	0%	30/07/14 08	19/08/14 05:00		43FS-10	0 days	0 days	0 days	0%								
45	Performance tuning	5 days	0%	20/08/14 08	26/08/14 05:00		44	0 days	0 days	0 days	0%								
46	Error Correction	5 days	0%	03/09/14 08	09/09/14 05:00		42, 45	0 days	0 days	0 days	0%								
47	User Acceptance Testing (UAT)	24 days	0%	10/09/14 08:00 am	14/10/14 05:00 pm		42, 46	0 days	0 days	0 days	0%								
48	Deploy	5 days	0%	21/10/14 08	27/10/14 05:00			0 days	0 days	0 days	0%								
49	BAU cycle OCTOBER	0 days	0%	20/10/14 05	20/10/14 05:00			0 days	0 days	0 days	0%								
50	Deploy to Production	5 days	0%	21/10/14 08	27/10/14 05:00		47, d:\s	0 days	0 days	0 days	0%								
51	Backport Phase 2 (Continuous) - COMPLETE	0 days	0%	27/10/14 05:00 pm	27/10/14 05:00 pm		50	0 days	0 days	0 days	0%								

Project: WCMS Integration Schedule
Date: 01/03/18 03:22 pm

Task

Split

Milestone

Summary

Project Summary

External Tasks

External Milestone

Inactive Task

Inactive Milestone

Inactive Summary

Manual Task

Duration-only

Manual Summary Rollup

Manual Summary

Start-only


Finish-only

Deadline

Progress

Page 2

ID	Task Name	Duration	% Comple	Start	Finish	Resource Names	Predecess	Work	Actual Work	Remaining Work	% Work Compl	Planned Release	Expected Release	May 2013				March 2015			
														1 May	1 April	1 March	1	1	1	1	
52	Design Components	70 days	0%	31/03/14 08:00	10/07/14 05:00			0 days	0 days	0 days	0%			28/01	08/07	16/12	26/05	03/11	13/04	21/09	
53	Application Requirements and Design (AR9) Updated	0 days	0%	28/03/14 05:00 pm	28/03/14 05:00 pm			0 days	0 days	0 days	0%										
54	Design Scoping	10 days	0%	31/03/14 08:00	11/04/14 05:00		d:\sche	0 days	0 days	0 days	0%										
55	Detailed Design	60 days	0%	14/04/14 08:00	10/07/14 05:00			0 days	0 days	0 days	0%										
56	Editor	60 days	0%	14/04/14 08:00	10/07/14 05:00		54	0 days	0 days	0 days	0%										
57	WCMS Database	60 days	0%	14/04/14 08:00	10/07/14 05:00		54	0 days	0 days	0 days	0%										
58	Content Preview Application	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%										
59	Content Application Engine	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%										
60	Content API	60 days	0%	14/04/14 08:00	10/07/14 05:00		54	0 days	0 days	0 days	0%										
61	Other Component Detail Design	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%										
62	Detail Design Complete	0 days	0%	10/07/14 05:00	10/07/14 05:00		54, 56,	0 days	0 days	0 days	0%										
63																					
64	NEWS Interfaces	179 days	0%	01/05/14 08:00	14/01/15 05:00			0 days	0 days	0 days	0%										
83	Radio Integration	105 days	0%	18/11/14 08:00	22/04/15 05:00			0 days	0 days	0 days	0%										
108	TV Integration	100 days	0%	10/02/15 08:00	02/07/15 05:00			0 days	0 days	0 days	0%										




Project: WCMS Integration Schedule
Date: 01/03/18 03:22 pm

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

ID	Task Name	Duration	% Complete	Start	Finish	Resource Names	Predecessors	Work	Actual Work	Remaining Work	% Work Complete	Planned Release	Expected Release	May 2013				March 2015						
														1 May	1 April	1 March	1	28/01	08/07	16/12	26/05	03/11	13/04	21/09
0	WCMS Integration Schedule	316 days	0%	31/03/14 08:00 am	02/07/15 05:00 pm			0 days	0 days	0 days	0%													
1	Commence Project	0 days	0%	31/03/14 08:00 am	31/03/14 08:00 am		d:\sche	0 days	0 days	0 days	0%													
2	Project start Up	20 days	0%	31/03/14 08:00 am	30/04/14 05:00 pm			0 days	0 days	0 days	0%													
3	Develop Business Case & High Level plan	20 days	0%	31/03/14 08:00 am	30/04/14 05:00 pm		1	0 days	0 days	0 days	0%													
4	Integration Requirements Design	20 days	0%	31/03/14 08:00 am	30/04/14 05:00 pm		3SS	0 days	0 days	0 days	0%													
5	NEWS Integration	199 days	0%	31/03/14 08:00 am	14/01/15 05:00 pm			0 days	0 days	0 days	0%													
6	NEWS & RADIO NATIONAL RESS support	87 days	0%	31/03/14 08:00 am	04/08/14 05:00 pm			0 days	0 days	0 days	0%													
7	Commence RESS support	0 days	0%	31/03/14 08:00 am	31/03/14 08:00 am			0 days	0 days	0 days	0%													
8	Analysis	5 days	0%	31/03/14 08:00 am	04/04/14 05:00 pm			0 days	0 days	0 days	0%													
9	Gap between New ViewDispatcher & Phase 2 Templating Framework	5 days	0%	31/03/14 08:00 am	04/04/14 05:00 pm		7	0 days	0 days	0 days	0%													
10	JSP Taglibraries(including PBE) for Freemarker Templates	5 days	0%	31/03/14 08:00 am	04/04/14 05:00 pm		7	0 days	0 days	0 days	0%													
11	RESS Support - solution design	5 days	0%	31/03/14 08:00 am	04/04/14 05:00 pm		7	0 days	0 days	0 days	0%													
12	Build	20 days	0%	07/04/14 08:00 am	07/05/14 05:00 pm			0 days	0 days	0 days	0%													
13	Build Front End Development environment	5 days	0%	07/04/14 08:00 am	11/04/14 05:00 pm		10, 11, 9	0 days	0 days	0 days	0%													
14	JSP Taglibraries(including PBE) for Freemarker Templates	5 days	0%	14/04/14 08:00 am	22/04/14 05:00 pm		13	0 days	0 days	0 days	0%													
15	schema changes for RESS & Freemarker template set	5 days	0%	14/04/14 08:00 am	22/04/14 05:00 pm		13	0 days	0 days	0 days	0%													
16	logical solution in RESS	15 days	0%	14/04/14 08:00 am	07/05/14 05:00 pm		13	0 days	0 days	0 days	0%													
17	CSS & JavaScript framework	5 days	0%	14/04/14 08:00 am	22/04/14 05:00 pm		13	0 days	0 days	0 days	0%													
18	Editor	5 days	0%	23/04/14 08:00 am	30/04/14 05:00 pm		15	0 days	0 days	0 days	0%													
19	Responsive demo Freemarker Templates	5 days	0%	01/05/14 08:00 am	07/05/14 05:00 pm		18	0 days	0 days	0 days	0%													
20	Testing	50 days	0%	08/05/14 08:00 am	17/07/14 05:00 pm			0 days	0 days	0 days	0%													
21	Automation Tests	20 days	0%	08/05/14 08:00 am	04/06/14 05:00 pm		12	0 days	0 days	0 days	0%													

Project: WCMS Integration Schedule
Date: 01/03/18 03:23 pm

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline
Split		External Tasks		Inactive Summary		Manual Summary		Progress
Milestone		External Milestone		Manual Task		Start-only		Finish-only
Summary		Inactive Task		Duration-only		Finish-only		Finish-only

ID	Task Name	Duration	% Complete	Start	Finish	Resource Names	Predecessors	Work	Actual Work	Remaining Work	% Work Complete	Planned Release	Expected Release	May 2013					March 2015				
														1 May					1 March				
														28/01	08/07	16/12	26/05	03/11	13/04	21/09	1		
22	Regression testing analysis	10 days	0%	08/05/14 08:00 am	21/05/14 05:00 pm		12	0 days	0 days	0 days	0%												
23	Regression testing	20 days	0%	22/05/14 08	19/06/14 05:00		22	0 days	0 days	0 days	0%												
24	Error Correction	20 days	0%	08/05/14 08	04/06/14 05:00		21SS	0 days	0 days	0 days	0%												
25	Performance testing	15 days	0%	22/05/14 08	12/06/14 05:00		24FS-1C	0 days	0 days	0 days	0%												
26	Performance tuning	5 days	0%	13/06/14 08	19/06/14 05:00		25	0 days	0 days	0 days	0%												
27	Error Correction	5 days	0%	20/06/14 08	26/06/14 05:00		23, 26	0 days	0 days	0 days	0%												
28	User Acceptance Testing (UAT)	15 days	0%	27/06/14 08:00 am	17/07/14 05:00 pm		23, 27	0 days	0 days	0 days	0%												
29	Deploy	5 days	0%	29/07/14 08	04/08/14 05:00			0 days	0 days	0 days	0%												
30	BAU cycle July	0 days	0%	28/07/14 05	28/07/14 05:00			0 days	0 days	0 days	0%												
31	Deploy to Production	5 days	0%	29/07/14 08	04/08/14 05:00		28, d:s	0 days	0 days	0 days	0%												
32	NEWS & RADIO NATIONAL RESS support - COMPLETE	0 days	0%	04/08/14 05:00 pm	04/08/14 05:00 pm		31	0 days	0 days	0 days	0%												
33	RESS Support - COMPLETE	0 days	0%	04/08/14 05	04/08/14 05:00		32	0 days	0 days	0 days	0%												
34	Part B (Task 2) RESS Support - COMPLETE	0 days	0%	22/10/14 05:00 pm	22/10/14 05:00 pm		32	0 days	0 days	0 days	0%												
35	Backport Phase 2 (Continuous)	146 days	0%	31/03/14 08	27/10/14 05:00			0 days	0 days	0 days	0%												
36	Analysis	50 days	0%	31/03/14 08	12/06/14 05:00		7SS	0 days	0 days	0 days	0%												
37	Build	48 days	0%	15/05/14 08	22/07/14 05:00			0 days	0 days	0 days	0%												
38	Port of Phase 2	48 days	0%	15/05/14 08	22/07/14 05:00		36FS-2C	0 days	0 days	0 days	0%												
39	Testing	50 days	0%	16/07/14 08	23/09/14 05:00			0 days	0 days	0 days	0%												
40	Automation Tests	48 days	0%	08/05/14 08	15/07/14 05:00		36SS, 1	0 days	0 days	0 days	0%												
41	Regression testing analysis	10 days	0%	23/07/14 08:00 am	05/08/14 05:00 pm		38	0 days	0 days	0 days	0%												
42	Regression testing	20 days	0%	06/08/14 08	02/09/14 05:00		41	0 days	0 days	0 days	0%												
43	Error Correction	20 days	0%	16/07/14 08	12/08/14 05:00		40SS	0 days	0 days	0 days	0%												
44	Performance testing	15 days	0%	30/07/14 08	19/08/14 05:00		43FS-1C	0 days	0 days	0 days	0%												
45	Performance tuning	5 days	0%	20/08/14 08	26/08/14 05:00		44	0 days	0 days	0 days	0%												
46	Error Correction	5 days	0%	03/09/14 08	09/09/14 05:00		42, 45	0 days	0 days	0 days	0%												
47	User Acceptance Testing (UAT)	24 days	0%	10/09/14 08:00 am	14/10/14 05:00 pm		42, 46	0 days	0 days	0 days	0%												
48	Deploy	5 days	0%	21/10/14 08	27/10/14 05:00			0 days	0 days	0 days	0%												
49	BAU cycle OCTOBER	0 days	0%	20/10/14 05	20/10/14 05:00			0 days	0 days	0 days	0%												
50	Deploy to Production	5 days	0%	21/10/14 08	27/10/14 05:00		47, d:s	0 days	0 days	0 days	0%												
51	Backport Phase 2 (Continuous) - COMPLETE	0 days	0%	27/10/14 05:00 pm	27/10/14 05:00 pm		50	0 days	0 days	0 days	0%												

Project: WCMS Integration Schedule
Date: 01/03/18 03:23 pm


Task: Project Summary: Inactive Milestone: Manual Summary Rollup: Deadline:

Split: External Tasks: Inactive Summary: Manual Summary: Progress:

Milestone: External Milestone: Manual Task: Start-only:

Summary: Inactive Task: Duration-only: Finish-only:

ID	Task Name	Duration	% Comple	Start	Finish	Resource Names	Predecessors	Work	Actual Work	Remaining Work	% Work Compl	Planned Release	Expected Release	May 2013				March 2015						
														1 May	1 April	1 March	1	28/01	08/07	16/12	26/05	03/11	13/04	21/09
52	Design Components	70 days	0%	31/03/14 08:00 am	10/07/14 05:00 pm			0 days	0 days	0 days	0%													
53	Application Requirements and Design (AR9) Updated	0 days	0%	28/03/14 05:00 pm	28/03/14 05:00 pm			0 days	0 days	0 days	0%													
54	Design Scoping	10 days	0%	31/03/14 08:00 am	11/04/14 05:00 pm		d:\sche	0 days	0 days	0 days	0%													
55	Detailed Design	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm			0 days	0 days	0 days	0%													
56	Editor	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%													
57	WCMS Database	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%													
58	Content Preview Application	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%													
59	Content Application Engine	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%													
60	Content API	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%													
61	Other Component Detail Design	60 days	0%	14/04/14 08:00 am	10/07/14 05:00 pm		54	0 days	0 days	0 days	0%													
62	Detail Design Complete	0 days	0%	10/07/14 05:00 pm	10/07/14 05:00 pm		54, 56,	0 days	0 days	0 days	0%													
63																								
64	NEWS Interfaces	179 days	0%	01/05/14 08:00 am	14/01/15 05:00 pm			0 days	0 days	0 days	0%													
83	Radio Integration	105 days	0%	18/11/14 08:00 am	22/04/15 05:00 pm			0 days	0 days	0 days	0%													
108	TV Integration	100 days	0%	10/02/15 08:00 am	02/07/15 05:00 pm			0 days	0 days	0 days	0%													



Project: WCMS Integration Schedule
Date: 01/03/18 03:23 pm

Task		Project Summary		Inactive Milestone		Manual Summary Rollup		Deadline	
Split		External Tasks		Inactive Summary		Manual Summary		Progress	
Milestone		External Milestone		Manual Task		Start-only			
Summary		Inactive Task		Duration-only		Finish-only			

WCMS Technology Foundation Plan

	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
1	WCMS Requirements	190 days	01/07/13 08:	C 28/03/14 05:			
2	Application Requirements and Design (AR9) Signed off	190 days	01/07/13 08:	C 28/03/14 05:		18FS-10 days, 20,	
3	Application Requirements and Design (AR9) Updated	0 days	28/03/14 05:	C 28/03/14 05: 2		152	
4	Application Requirements and Design (AR9) Updated	0 days	28/03/14 05:	C 28/03/14 05: 2		152	
5	Environment Requirements (AR10) Signed off	170 days	01/07/13 08:	C 28/02/14 05:		18FS-10 days	
6	✓ Release Management Requirements (AR11) Signed off	131 days	01/07/13 08:	C 03/01/14 05:		12FS-9 days, 21FS	
7	✓ Infrastructure Requirements (AR1) signed off	120 days	01/07/13 08:	C 13/12/13 05:		15	
8	✓ Load Balancing & Traffic Routing Requirements (AR3) signed off	94 days	01/07/13 08:00 am	07/11/13 05:00 pm		15FS-10 days, 13	
9	✓ Monitoring System Requirements (AR2) signed off	85 days	01/07/13 08:	C 25/10/13 05:		20, 14	
10							
11	Core Design Activities	124 days	21/10/13 08:	C 17/04/14 05:			
12	✓ Gartner Review of Release Management Requirements	75 days	08/11/13 08:00 am	27/02/14 05:00 pm	6FS-9 days		
13	✓ Gartner Review of Load Balancing	61 days	08/11/13 08:	C 07/02/14 05: 8			
14	 Gartner Review of Monitoring	85 days	28/10/13 08:	C 28/02/14 05: 9			
15	✓ Production Design (Incl Load Balancing)	5 days	21/10/13 08:	C 25/10/13 05: 2FS-15 days, 7, 8, 92, 16, 57, 34			
16	Core Media Review of Design	15 days	06/02/14 08:	C 26/02/14 05: 15, 2FS-5 days	23, \\nucfile01\c		
17	Core Media Review of Design	0 days	26/02/14 05:	C 26/02/14 05: 16		152	
18	✓ Environments (non-Prod) Design	10 days	25/11/13 08:	C 06/12/13 05: 2FS-10 days, 5FS 50, 33, 26FS+1 d			
19	✓ Lab Access Design	48 days	09/12/13 08:	C 19/02/14 05: 18		50	
20	 Monitoring Design	49 days	10/02/14 08:	C 17/04/14 05: 2, 9		65FS-9 days	

WCMS Technology Foundation Plan

	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
21	✓ Deployment Process POCs	44 days	25/11/13 08:00	30/01/14 05:00	6FS-5 days	22	
22	Deployment Process Design	40 days	31/01/14 08:00	27/03/14 05:00	21	83	
23	Review AR9 Requirements and Core Media Review for impact	2 days	31/03/14 08:00 am	01/04/14 05:00 pm	2, 16		
24							
25	✓ Performance Test Environment (TA&D 13-07-17)	32 days	10/12/13 08:00	29/01/14 05:00			
32	Non-prod Environment Build (TA&D 13-04-08)	101.5 days	22/11/13 08:00	21/04/14 12:00			
49	LAB Access (TA&D 13-02-03)	52.5 days	20/02/14 08:00	05/05/14 12:00			
56	✓ Production Design Review & Build (TA&D 13-07-11)	38 days	28/10/13 08:00	18/12/13 05:00			
64	Monitoring Systems (TA&D 13-05-15)	100.5 days	02/04/14 08:00	20/08/14 12:00			
82	Enhance Deployment Process (TA&D 13-07-17)	31 days	28/03/14 08:00	09/05/14 05:00			
83	HLD & SCE Sign off	1 day	28/03/14 08:00	28/03/14 05:00	22	84, 85	
84	Order Hardware & Delivery	0 days	28/03/14 05:00	28/03/14 05:00	83	86	
85	Detailed Design	5 days	31/03/14 08:00	04/04/14 05:00	83	86	
86	Build Solution in lab	5 days	07/04/14 08:00	11/04/14 05:00	84, 85, 42	87	
87	Configure Solution in Lab	5 days	14/04/14 08:00	18/04/14 05:00	86	88	
88	Build solution in production	5 days	21/04/14 08:00	25/04/14 05:00	87	89	
89	Configure solution in production	10 days	28/04/14 08:00	09/05/14 05:00	88	90	
90	Enhance Deployment Process Complete	0 days	09/05/14 05:00	09/05/14 05:00	89	133	
91	Layer 7 (Caching-AR3) Traffic Routing (TA&D 13-04-09)	130 days	28/10/13 08:00	02/05/14 05:00			
105							
106	Key Foundation Milestones	292.5 days	01/07/13 08:00	20/08/14 12:00			

WCMS Technology Foundation Plan

	Task Name	Duration	Start	Finish	Predecessors	Successors	% Comple
107	Application Requirements and Design (AR9) Updated	0 days	01/07/13 08:C	01/07/13 08:			
108 ✓	Perf Test Environment Ready	0 days	29/01/14 05:C	29/01/14 05: 30		d:\schedule\mast	
109	Perf Test Environment Ready	0 days	29/01/14 05:C	29/01/14 05: 108			
110	Perf Test Environment Ready	0 days	29/01/14 05:C	29/01/14 05: 108			
111	Perf Test Environment Ready	0 days	29/01/14 05:C	29/01/14 05: 108			
112 ✓	UAT Environment Ready	0 days	12/02/14 05:C	12/02/14 05: 36, 99		d:\schedule\mast	
113	UAT Environment Ready	0 days	12/02/14 05:C	12/02/14 05: 112			
114	UAT Environment Ready	0 days	12/02/14 05:C	12/02/14 05: 112			
115	UAT Environment Ready	0 days	12/02/14 05:C	12/02/14 05: 112			
116 ✓	Test Environment Ready	0 days	13/02/14 05:C	13/02/14 05: 38		d:\schedule\mast	
117	Test Environment Ready	0 days	13/02/14 05:C	13/02/14 05: 116			
118	Test Environment Ready	0 days	13/02/14 05:C	13/02/14 05: 116			
119	Test Environment Ready	0 days	13/02/14 05:C	13/02/14 05: 116			
120	Training Environment Ready	0 days	05/03/14 05:C	05/03/14 05: 44			
121	Staging Environment Ready	0 days	07/04/14 12:C	07/04/14 12: 45		d:\schedule\mast	
122	Staging Environment Ready	0 days	07/04/14 12:C	07/04/14 12: 121			
123	Staging Environment Ready	0 days	07/04/14 05:C	07/04/14 05: 121			
124	Staging Environment Ready	0 days	07/04/14 12:C	07/04/14 12: 121			
125	Production Environment Ready	0 days	18/04/14 05:C	18/04/14 05: 63, 102		d:\schedule\mast	
126	Production Environment Ready	0 days	18/04/14 05:C	18/04/14 05: 125			
127	Production Environment Ready	0 days	18/04/14 05:C	18/04/14 05: 125			
128	Production Environment Ready	0 days	18/04/14 05:C	18/04/14 05: 125			

WCMS Technology Foundation Plan

	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
129	Lab Access Complete	0 days	05/05/14 12:00	05/05/14 12:55		d:\schedule\mast	
130	Lab Access Complete	0 days	05/05/14 12:00	05/05/14 12:129			
131	Lab Access Complete	0 days	05/05/14 05:00	05/05/14 05:129			
132	Lab Access Complete	0 days	05/05/14 12:00	05/05/14 12:129			
133	Enhanced Deployment Processes Complete	0 days	09/05/14 05:00	09/05/14 05:90		d:\schedule\mast	
134	Enhanced Deployment Processes Complete	0 days	09/05/14 05:00	09/05/14 05:133		181	
135	Enhanced Deployment Processes Complete	0 days	09/05/14 05:00	09/05/14 05:133		181	
136	Enhanced Deployment Processes Complete	0 days	09/05/14 05:00	09/05/14 05:133			
137	Layer 7 Routing Complete	0 days	02/05/14 05:00	02/05/14 05:104		d:\schedule\mast	
138	Layer 7 Routing Complete	0 days	02/05/14 05:00	02/05/14 05:137			
139	Layer 7 Routing Complete	0 days	02/05/14 05:00	02/05/14 05:137			
140	Layer 7 Routing Complete	0 days	02/05/14 05:00	02/05/14 05:137			
141	Monitoring Systems (Tactical) Complete	0 days	02/07/14 12:00	02/07/14 12:73		d:\schedule\mast	
142	Monitoring Systems (Tactical) Complete	0 days	02/07/14 12:00	02/07/14 12:141			
143	Monitoring Systems (Tactical) Complete	0 days	02/07/14 12:00	02/07/14 12:141			
144	Monitoring Systems (Tactical) Complete	0 days	02/07/14 12:00	02/07/14 12:141			
145	Monitoring Systems Complete	0 days	20/08/14 12:00	20/08/14 12:81		d:\schedule\mast	
146	Monitoring Systems Complete	0 days	20/08/14 12:00	20/08/14 12:145			
147	Monitoring Systems Complete	0 days	20/08/14 12:00	20/08/14 12:145			
148	Monitoring Systems Complete	0 days	20/08/14 12:00	20/08/14 12:145			
149							
150	Consolidate NEWS and Radio National & View Dispatcher	65 days	03/03/14 08:00	30/05/14 05:00			

WCMS Technology Foundation Plan

	Task Name	Duration	Start	Finish	Predecessors	Successors	% Complete
151	Core Media Review of Design	0 days	26/02/14 05:C	26/02/14 05: 16		152	
152	✓ Commence Part 1 Consolidation	0 days	03/03/14 08:C	03/03/14 08: \\nucfile01\c	153		
153	✓ Execution Test	10 days	10/03/14 08:C	21/03/14 05: 152		155FS-5 days, 156	
154	Analysis	5 days	17/03/14 08:C	21/03/14 05:			
155	BAU impact analysis	5 days	17/03/14 08:C	21/03/14 05: 153FS-5 days			
156	Business logic analysis	5 days	17/03/14 08:C	21/03/14 05: 153FS-5 days		161SS-5 days	
157	Template analysis	5 days	17/03/14 08:C	21/03/14 05: 153FS-5 days			
158	✓ Multi-Tenant Analysis	5 days	17/03/14 08:C	21/03/14 05: 153FS-5 days			
159	Consolidate	20 days	17/03/14 08:C	11/04/14 05:			
160	Merge NEWS and Radio National	20 days	17/03/14 08:C	11/04/14 05: 153FS-5 days		171SS, 172SS	
161	Migrate business logic	20 days	17/03/14 08:C	11/04/14 05: 156SS-5 days, 157		171SS, 172SS	
162	View Dispatcher & Freemarker Framework	8 days	24/03/14 08:C	02/04/14 05:			
163	✓ Analysis	3 days	24/03/14 08:C	26/03/14 05:			
164	✓ View dispatcher	3 days	24/03/14 08:C	26/03/14 05: 153		167	
165	✓ Freemarker Templates support	3 days	24/03/14 08:C	26/03/14 05: 153		167	
166	Build	5 days	27/03/14 08:C	02/04/14 05:			
167	✓ viewdispatcher for Freemarker Templates	5 days	27/03/14 08:C	02/04/14 05: 164, 165		168FS-5 days, 169	
168	Freemarker Templates demo templates	3 days	27/03/14 08:C	31/03/14 05: 167FS-5 days		169	
169	Freemarker Framework - Complete	0 days	02/04/14 05:C	02/04/14 05: 167, 168			
170	Testing	50 days	17/03/14 08:C	23/05/14 05:			
171	Test (Touch Points)	20 days	17/03/14 08:C	11/04/14 05: 160SS, 161SS		174SS	
172	Regression testing analysis	10 days	17/03/14 08:C	28/03/14 05: 161SS, 160SS		173	

WCMS Technology Foundation Plan

	 Task Name	Duration	Start	Finish	Predecessors	Successors	% Comple
173	Regression testing	20 days	31/03/14 08:	25/04/14 05:	172	178, 177	
174	Error Correction	20 days	17/03/14 08:	11/04/14 05:	171SS	175FS-10 days	
175	Performance testing	15 days	31/03/14 08:	18/04/14 05:	174FS-10 days	176	
176	Performance tuning	5 days	21/04/14 08:	25/04/14 05:	175	177	
177	Error Correction	5 days	28/04/14 08:	02/05/14 05:	176, 173	178	
178	User Acceptance Testing (UAT)	15 days	05/05/14 08:	23/05/14 05:	177, 173	181	
179	Deploy	5 days	26/05/14 08:	30/05/14 05:			
180	BAU cycle May	0 days	26/05/14 08:	26/05/14 08:		181	
181	Deploy to Production	5 days	26/05/14 08:	30/05/14 05:	178, \\nucfile01'	182	
182	NEWS and Radio National Consolidation - COMPLETE	0 days	30/05/14 05:	30/05/14 05:	181	\\nucfile01\cwpd	
183	NEWS and Radio National Consolidation - COMPLETE	0 days	30/05/14 05:	30/05/14 05:	182		
184	NEWS and Radio National Consolidation - COMPLETE	0 days	05/06/14 05:	05/06/14 05:	182		

WCMS Technology Foundation Plan

Resource Names	Phase	Plai Exp
WCMS	Foundat	
WCMS	Foundat	
WCMS	Foundat	
WCMS	Foundat	
WCMS	Foundat	
WCMS	Foundat	
	Foundat	
Enterprise Architecture	Foundat	
Enterprise Architect	Foundat	
Enterprise Architect	Foundat	
Architecture	Foundat	
Core Media	Foundat	
Architecture	Foundat	
Architecture	Foundat	
Architecture	Foundat	

WCMS Technology Foundation Plan

Resource Names	Phase	Plai Exp
WCMS, Architectur	Foundat	
Architecture	Foundat	
Architecture	Foundat	
	Foundat	
	Foundat	
	Foundat	
	Foundat	
	Foundat	
	Foundat	
WCMS	Foundat	
Development	Foundat	
Development	Foundat	
Development	Foundat	
Development	Foundat	
Development	Foundat	
Development	Foundat	
	Foundat	
	Foundat	
	Foundat	

WCMS Technology Foundation Plan

Resource Names	Phase	Plat Exp
	Foundat	
	Foundat	
	Foundat	
	Foundat	
	Foundat	
	Foundat	

WCMS Technology Foundation Plan

Resource Names	Phase	Pla	Exp
	Foundat		
	Foundat		
	Foundat		
	Foundat		
	Foundat		

